

**WEEKLY PROGRESS REPORT – TRC SOLUTIONS**

**Gowanus Canal Turning Basin 4 Dredging and Capping Pilot Study  
Brooklyn, New York**

**Project number: 283126**

**Period: November 27 to December 1, 2017**

**Date of Report: December 7, 2017**

**Rev: 0**

**Prepared For: Gowanus Environmental Remediation Trust**



## **On-Site Activities Conducted During Week:**

### *Sevenson Environmental Services (SES)*

#### Sheet Pile Installation

- Installation of 16.5 pairs of sheet pile to approximate Station 7+60.
- Work suspended by GERT on 11/29 to collect and evaluate data and implement corrective actions in response to observed movement of the existing bulkhead in accordance with the specifications.

#### Access Dredging

- One barge (Weeks 80) of stabilized sediment transferred to Clean Earth Claremont and transported to Waste Management Fairless Hills for beneficial reuse (i.e., daily cover). Paint filter testing of stabilized material performed as required by Clean Earth prior to shipment off-site.

#### Water Treatment and Monitoring

- No discharge of treated water during the week.
- Continue construction of winterization structures

#### Turbidity Monitoring

- Turbid water not observed migrating from the 4<sup>th</sup> Street Turning Basin.

#### Vibration Monitoring (subcontractor – Vibra-Tech)

- Operated and maintained five (5) stationary vibration monitors. Two (2) stationary monitors located on the south side of the canal, one (1) stationary monitor located on the north side of the canal, two (2) stationary monitors located on the 3<sup>rd</sup> Avenue Bridge abutments. Additionally, employed two (2), at a minimum, portable vibration monitors to measure vibration levels within 15 feet of the sheet pile installation work.
- Performed daily crack gauge inspections at 386 3<sup>rd</sup> Avenue.
- No exceedances of the peak particle velocity level specified in the Contract Documents (0.40 inches per second) during the week.
- Exceedance of the acceleration level specified in the Contract Documents (0.1 g) occurred during sheet pile installation on 11/27/17 due to obstruction encountered during installation.

### *Quality Assurance - Geosyntec*

- No exceedance of turbidity trigger level of a measurement over a one-hour period of the sentinel buoy 20 nephelometric turbidity units (NTUs) greater than the ambient buoy during access dredging.
- Measurements for 11/27/17:
  - Daily average for ambient buoy – 6.3 NTU
  - Daily average for sentinel buoy – 6.9 NTU
  - Greatest difference between ambient and sentinel buoy during 15-minute interval – 5.1 NTU at 1615
- Measurements for 11/28/17:
  - Daily average for ambient buoy – 5.8 NTU
  - Daily average for sentinel buoy – 6.1 NTU
  - Greatest difference between ambient and sentinel buoy during 15-minute interval – 2.5 NTU at 1615.
- Measurements for 11/29/17:
  - Daily average for ambient buoy – 7.5 NTU
  - Daily average for sentinel buoy – 7.4 NTU
  - Greatest difference between ambient and sentinel buoy during 15-minute interval – 3.5 NTU at 1310.



- Measurements for 11/30/17:
  - Daily average for ambient buoy – 7.9 NTU
  - Daily average for sentinel buoy – 9.3 NTU
  - Greatest difference between ambient and sentinel buoy during 15-minute interval – 6.7 NTU at 1300.
- Measurements for 12/01/17:
  - Daily average for ambient buoy – 8.3 NTU
  - Daily average for sentinel buoy – 8.7 NTU
  - Greatest difference between ambient and sentinel buoy during 15-minute interval – 2.7 NTU at 1130.

*Community Air Monitoring Program – TRC CAMP*

- Operated and maintained two (2) air monitoring stations at the upland staging area and five (5) monitoring station at the 4<sup>th</sup> Street Turning Basin Area.
- No exceedances of particulate matter of 10 microns in diameter or smaller (PM<sub>10</sub>) or total volatile organic compounds (TVOC) of the action level of 150 micrograms per cubic meter or 1,000 parts per billion, respectively.
- Maximum weekly measurements of PM<sub>10</sub> in µg/m<sup>3</sup>
  - Station 1 – 29 µg/m<sup>3</sup> recorded on 11/30/17
  - Station 2 – 79 µg/m<sup>3</sup> recorded on 11/28/17
  - Station 3 – <1 µg/m<sup>3</sup> recorded throughout week
  - Station 4 – 21 µg/m<sup>3</sup> recorded on 11/28/17
  - Station 5 – 19 µg/m<sup>3</sup> recorded on 11/28/17
  - Station 6 – 14 µg/m<sup>3</sup> recorded on 11/28/17
  - Station 7 – <1 µg/m<sup>3</sup> recorded throughout week
- Maximum weekly measurements of TVOC in ppb
  - Station 1 – 85 ppb recorded on 11/29/17
  - Station 2 – 30 ppb recorded on 11/30/17
  - Station 3 – 135 ppb recorded on 11/28/17
  - Station 4 – 38 ppb recorded on 11/28/17
  - Station 5 – 61 ppb recorded on 11/30/17
  - Station 6 – 47 ppb recorded on 11/28/17
  - Station 7 – 108 ppb recorded on 11/28/17
- No real-time readings of hydrogen sulfide, ammonia, or formaldehyde greater than instrument detection limit throughout the week.
- 24-hour sample collected at ST-1 on 11/29 through 11/30 and at ST-6 (collocated) on 11/30 through 12/01. Laboratory turnaround time is 10 business days.

*Noise and Vibration Monitoring – Wilson Ihrig*

- Operated and maintained three (3) noise monitors: NM-1 (north side of canal on Whole Foods promenade), NM-2 (south side of canal on southeast corner of 386 3rd Avenue), and NM-3 (southeast corner of Whole Foods at 3rd Avenue Bridge).
- Exceedances of the hourly Leq noise limit of 80 dBA during sheet pile installation measured at all monitors. Mitigating measures being evaluated and implemented. Noise monitor NM-1 located within exclusion zone and not indicative of public exposure.
- Greatest hourly Leq noise measurements
  - Northern monitor (NM-1) – 100.1 dBA during 1100-1200 on 11/27/17
  - Southern monitor (NM-2) – 100 dBA during 1300-1400 on 11/29/17
  - 3<sup>rd</sup> Avenue Bridge monitor (NM-3) – 90.9 dBA during 1000-1100 on 11/29/17



- No exceedances of the commercial and industrial structures vibration criterion of 2.0 inches per second peak particle velocity.
- Greatest peak particle velocity measurements
  - Northern monitor (NM-1) – 0.0363 in/sec event between 1100 and 1200 on 11/28/17
  - Southern monitor (NM-2) – 0.0512 in/sec event between 1000 and 1100 on 11/28/17

*Cultural Natural Resource Monitoring – Archeology and Historic Resource Services (AHRS)*

- No inspections conducted during week and expected prior to commencing Phase 1 dredging.

**Two-Week Look Ahead:**

- Severson:
  - Continue installation of steel sheet pile bulkhead supports.
  - Perform vibration, benchmark, and optical monitoring of bulkheads and surrounding structures.
  - Install swing gate along Huntington Street.
  - Reassemble drum storage pad.
  - Continue installation of winterization structures for dredged water treatment system.
- Geosyntec – Perform construction quality assurance responsibilities.
- TRC CAMP Monitoring – Perform community air monitoring.
- Wilson Ihrig – Perform noise and vibration monitoring.
- Emilcott – No activities planned.
- AHRS – No activities planned.

**Project Milestones:** Key project milestones either established or completed this period include the following:

- No milestones achieved during period.

Attachments:

1. Geosyntec In-Canal Water Quality Monitoring Weekly Data Summary
2. TRC Weekly CAMP Report
3. Wilson Ihrig Weekly Noise and Vibration Monitoring Report
4. AHRS Weekly Report (no activities during current week)
5. Water Treatment System Monitoring Analytical Laboratory Data (no activities during current week)
6. Cumulative Dredged Material Chart (no activities during current week)



<b>Client Name:</b> Gowanus ERT	<b>Site Location:</b> TB-4 Pilot Study	<b>Project No.:</b> 283126.0000.0001
------------------------------------	-------------------------------------------	-----------------------------------------

<b>Photo No.</b> 001	<b>Date</b> 11-27-2107
-------------------------	---------------------------

**Description**  
Installation of sheet pile for the day.



<b>Photo No.</b> 002	<b>Date</b> 11-28-2017
-------------------------	---------------------------

**Description**  
Aligning the last pin pile for the falsework.



<b>Client Name:</b> Gowanus ERT	<b>Site Location:</b> TB-4 Pilot Study	<b>Project No.:</b> 283126.0000.0001
------------------------------------	-------------------------------------------	-----------------------------------------

<b>Photo No.</b> 003	<b>Date</b> 11-28-2017
-------------------------	---------------------------

**Description**  
Setting up survey station.



<b>Photo No.</b> 004	<b>Date</b> 11-29-2017
-------------------------	---------------------------

**Description**  
Finishing driving sheet pile.



<b>Client Name:</b> Gowanus ERT	<b>Site Location:</b> TB-4 Pilot Study	<b>Project No.:</b> 283126.0000.0001
------------------------------------	-------------------------------------------	-----------------------------------------

<b>Photo No.</b> 005	<b>Date</b> 11-29-2107
-------------------------	---------------------------

**Description**  
Driving single sheet to help align the steel sheet pile.



<b>Photo No.</b> 006	<b>Date</b> 11-30-2017
-------------------------	---------------------------

**Description**  
View of completed cribbing.



**GEOSYNTEC IN-CANAL WATER QUALITY MONITORING WEEKLY DATA SUMMARY**



# **GOWANUS CANAL SUPERFUND SITE DREDGING AND CAPPING PILOT STUDY Water Quality Monitoring Weekly Data Summary**

Week of November 27<sup>th</sup>, 2017

## **Report Contents**

- Scope of Monitoring
- Turbidity Buoy Data
- Handheld Measurements
- Summary of Visual Observations
  - Report of Exceedances

*Prepared by*

**Geosyntec**   
consultants

engineers | scientists | innovators

**Beech and Bonaparte**   
engineering p.c.

*an affiliate of Geosyntec Consultants*

7 Graphics Drive, Suite 106  
Ewing, NJ 08628  
Project Number HPH106A (52)

## 1. SCOPE OF MONITORING

The following report summarizes water quality monitoring data collected during the week of November 27<sup>th</sup>, 2017. Two turbidity buoys were deployed to monitor turbidity during the pilot study. One turbidity buoy was deployed just outside of the 4<sup>th</sup> Street Turning Basin and is referred to as the sentinel buoy. A second turbidity buoy was deployed further upstream in RTA1 in order to monitor background turbidity unaffected by on-water construction activities. This turbidity buoy is referred to as the ambient buoy. A map indicating the approximate locations of the turbidity buoys is provided in Figure 1. Each turbidity buoy was equipped with a YSI 600 OMS water quality meter with optical turbidity sensor. The buoys were programmed such that readings were collected every 15 minutes. After each measurement, the turbidity data were transmitted to a FTP site via telemetry. This report provides the turbidity data collected every 15 minutes from both the ambient and sentinel buoys during each day between 7 AM and 5 PM during the week of November 27<sup>th</sup>. Average and maximum turbidity are also presented. No handheld measurements were collected during this reporting period. Visual observations of turbidity and sheen are summarized in Section 4. The data provided in this summary report have not yet been validated and should be considered preliminary.



## 2. TURBIDITY BUOY DATA

The following section provides turbidity data for the sentinel and ambient turbidity buoys from 7 AM to 5 PM from November 27<sup>th</sup> to December 1<sup>st</sup>, 2017. Turbidity buoys were temporarily offline for maintenance on the morning of November 29<sup>th</sup>. Background data prior to the start of dredging is provided in Appendix A. No exceedances to the rolling average threshold criteria were observed during the reporting period.

### 2.1 Monday, November 27<sup>th</sup>, 2017

Time (Local)	Ambient Turbidity (NTU)	Sentinel Turbidity (NTU)	Sentinel >Ambient (Y/N)	Time (Local)	Ambient Turbidity (NTU)	Sentinel Turbidity (NTU)	Sentinel >Ambient (Y/N)
11/27/2017 7:00	5.1	6.0	Y	11/27/2017 12:15	8.1	8.4	Y
11/27/2017 7:15	4.6	5.4	Y	11/27/2017 12:30	7.8	7.4	N
11/27/2017 7:30	5.0	6.8	Y	11/27/2017 12:45	7.2	8.5	Y
11/27/2017 7:45	5.9	6.0	Y	11/27/2017 13:00	7.4	8.4	Y
11/27/2017 8:00	6.1	9.4	Y	11/27/2017 13:15	5.7	8.5	Y
11/27/2017 8:15	6.1	7.8	Y	11/27/2017 13:30	5.1	5.8	Y
11/27/2017 8:30	7.4	6.5	N	11/27/2017 13:45	4.6	5.8	Y
11/27/2017 8:45	6.7	7.4	Y	11/27/2017 14:00	4.8	5.3	Y
11/27/2017 9:00	6.7	7.7	Y	11/27/2017 14:15	4.8	5.6	Y
11/27/2017 9:15	6.3	7.0	Y	11/27/2017 14:30	5.1	5.3	Y
11/27/2017 9:30	7.1	6.6	N	11/27/2017 14:45	5.0	5.1	Y
11/27/2017 9:45	7.7	7.0	N	11/27/2017 15:00	4.8	5.4	Y
11/27/2017 10:00	7.9	6.8	N	11/27/2017 15:15	4.6	5.5	Y
11/27/2017 10:15	8.3	7.7	N	11/27/2017 15:30	4.8	5.2	Y
11/27/2017 10:30	8.2	8.0	N	11/27/2017 15:45	5.3	5.7	Y
11/27/2017 10:45	10.7	8.0	N	11/27/2017 16:00	5.4	5.4	N
11/27/2017 11:00	7.3	8.3	Y	11/27/2017 16:15	4.8	9.9	Y
11/27/2017 11:15	8.5	7.7	N	11/27/2017 16:30	4.4	6.4	Y
11/27/2017 11:30	7.4	8.3	Y	11/27/2017 16:45	4.7	5.7	Y
11/27/2017 11:45	7.9	7.9	N	11/27/2017 17:00	5.2	6.8	Y
11/27/2017 12:00	8.3	8.0	N				

Average	6.3	6.9	Y
Maximum	10.7	9.9	N

**Notes:**

No exceedances to rolling average threshold criteria during reporting period

Values highlighted in green are greater than 20 NTU above the ambient buoy reading

Values highlighted in blue are greater than 40 NTU above the ambient buoy reading









### 3. HANDHELD MEASUREMENTS

No handheld measurements were collected for this reporting period.

### 4. SUMMARY OF VISUAL OBSERVATIONS


Visual observations are consistent with background conditions of the turning basin.

### 5. REPORT OF EXCEEDANCES

No exceedances of the water quality monitoring threshold criteria were met during the reporting period. Refer to the Water Quality Monitoring Plan for In-waterway Construction Activities (Geosyntec 2017) for further information regarding the Trigger and Action Criteria. Threshold criteria are summarized as follows:

- **Trigger criterion** – Any of the following:
  - The rolling average of the sentinel buoy turbidity measurements over a one-hour period exceeds the rolling average of the ambient buoy turbidity measurements by 20 NTU excluding any eliminated outlier measurements; or
  - Either an oil sheen or a turbidity plume is visually observed outside of engineering controls and in-waterway construction activities cannot be immediately excluded as the source.
- **Action criterion** – Any of the following:
  - The rolling average of the sentinel buoy turbidity measurements over a one-hour period exceeds the rolling average of the ambient buoy turbidity measurements by 40 NTU excluding any eliminated outlier measurements; or
  - Either an oil sheen or a turbidity plume is visually observed outside of engineering controls and in-waterway construction activities are readily identified as the source.

# **FIGURES**

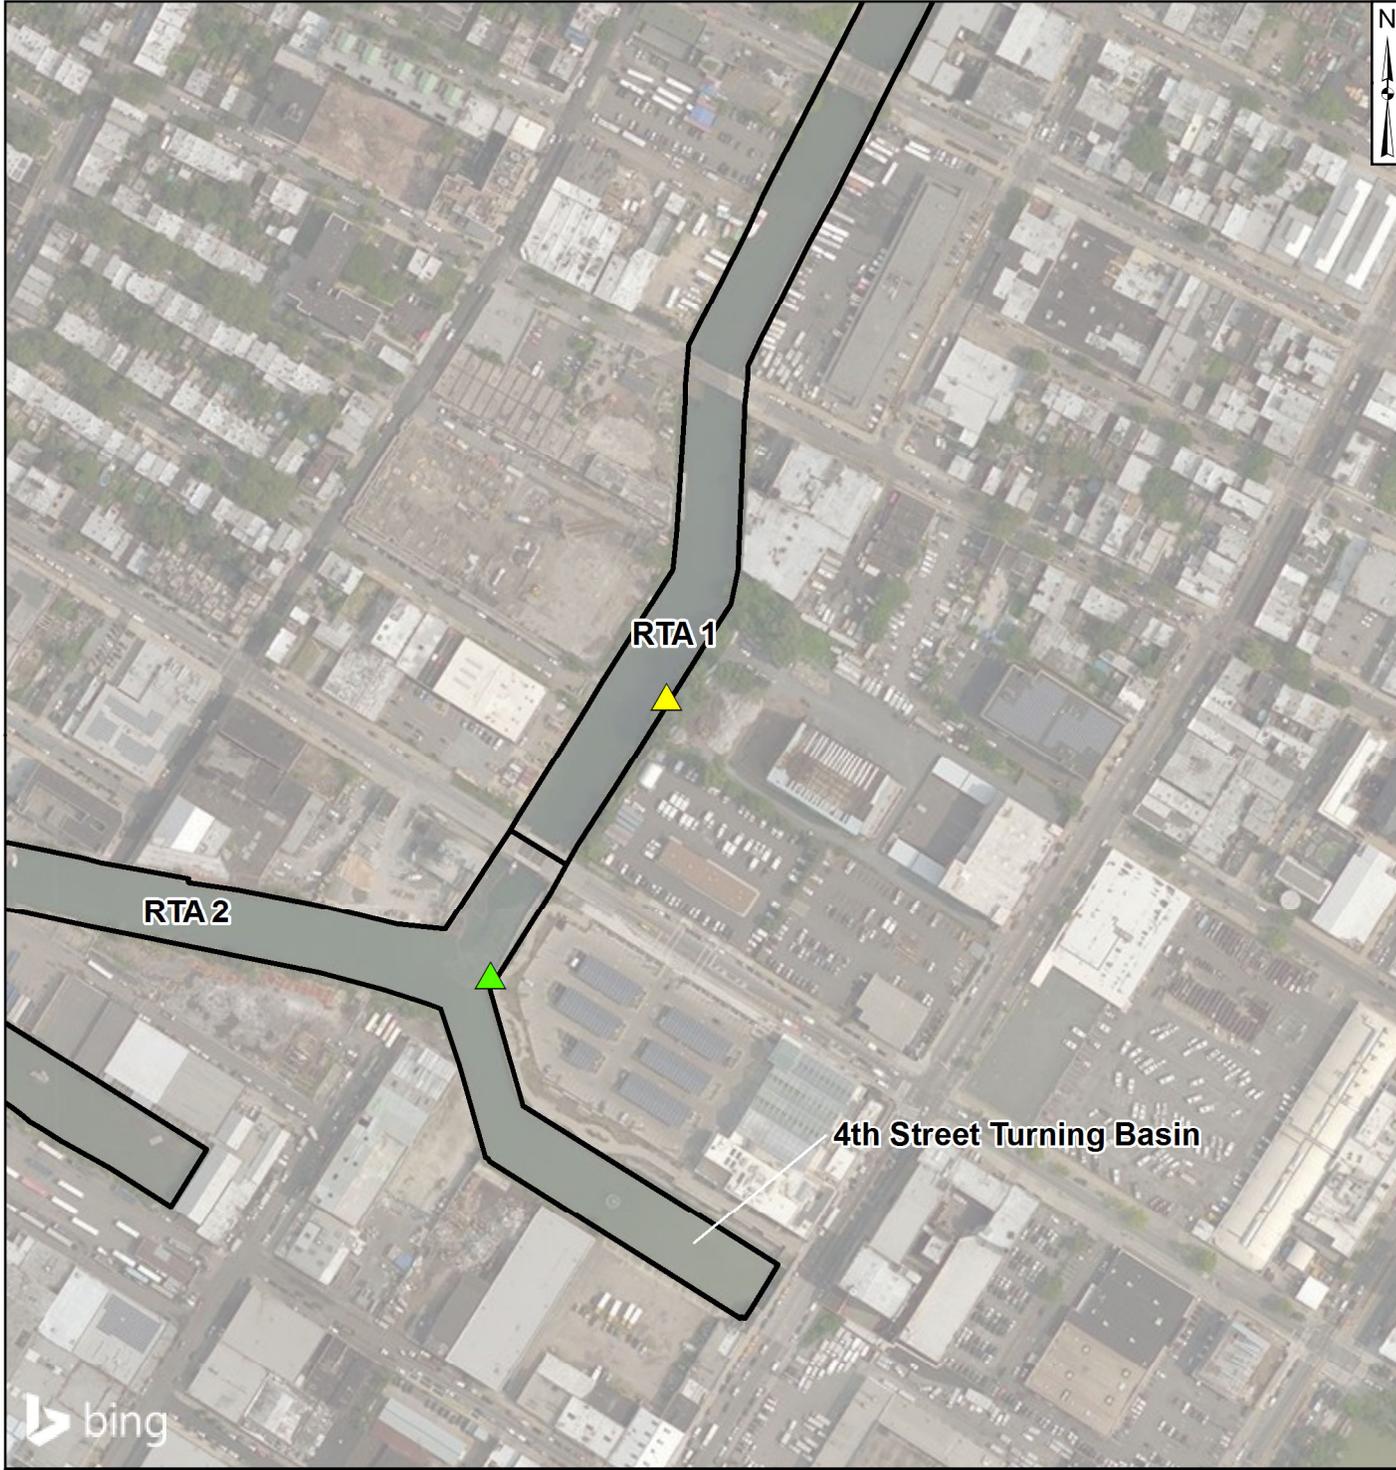

X:\03\_GIS\mxd\Canal\_Wide\_Turbidity\_Buoy\_Locations.mxd; acarnes; 10/19/2017



**Legend**

- Ambient Buoy
- Sentinel Buoy
- RTA Boundary



**Turbidity Buoy Locations**

Gowanus Canal, Brooklyn, NY

**Gowanus Canal Remedial Design Group** **Geosyntec** consultants **Beech and Bonaparte** engineering p.c.  
*an affiliate of Geosyntec Consultants*

**Figure**

**1**

Ewing, NJ

October 2017

**APPENDIX A**  
**PRE-DREDGE TURBIDITY BUOY DATA**

Time (Local)	Ambient Turbidity (NTU)	Sentinel Turbidity (NTU)	Sentinel> Ambient (Y/N)	Time (Local)	Ambient Turbidity (NTU)	Sentinel Turbidity (NTU)	Sentinel> Ambient (Y/N)	Time (Local)	Ambient Turbidity (NTU)	Sentinel Turbidity (NTU)	Sentinel> Ambient (Y/N)
10/3/2017 15:00	7.4	2.7	N	10/4/2017 4:30	4.8	7.1	Y	10/4/2017 18:00	6.9	2.7	N
10/3/2017 15:15	6.6	2.4	N	10/4/2017 4:45	5	6.3	Y	10/4/2017 18:15	7.2	2.7	N
10/3/2017 15:30	6.4	2.7	N	10/4/2017 5:00	4.7	6	Y	10/4/2017 18:30	7.8	3.4	N
10/3/2017 15:45	6.9	2	N	10/4/2017 5:15	5.1	6.4	Y	10/4/2017 18:45	8.2	4.4	N
10/3/2017 16:00	6.3	2.1	N	10/4/2017 5:30	5	7.3	Y	10/4/2017 19:00	7.5	3.1	N
10/3/2017 16:15	6.5	2.4	N	10/4/2017 5:45	5.4	7.8	Y	10/4/2017 19:15	8.7	3.6	N
10/3/2017 16:30	7.1	2.9	N	10/4/2017 6:00	5.5	8.3	Y	10/4/2017 19:30	8.7	4.5	N
10/3/2017 16:45	6.1	2.8	N	10/4/2017 6:15	5.2	9	Y	10/4/2017 19:45	9.4	4.1	N
10/3/2017 17:00	7	2.8	N	10/4/2017 6:30	5.8	7.2	Y	10/4/2017 20:00	8.4	4	N
10/3/2017 17:15	7	4.4	N	10/4/2017 6:45	5.4	8.8	Y	10/4/2017 20:15	8.2	4	N
10/3/2017 17:30	7	4.7	N	10/4/2017 7:00	5.5	8	Y	10/4/2017 20:30	9	3.6	N
10/3/2017 17:45	6.3	4	N	10/4/2017 7:15	5.6	7.5	Y	10/4/2017 20:45	8.4	3.5	N
10/3/2017 18:00	6.5	6.9	Y	10/4/2017 7:30	6.9	7.2	Y	10/4/2017 21:00	9.5	4.7	N
10/3/2017 18:15	7.8	6.7	Y	10/4/2017 7:45	6.8	6.1	N	10/4/2017 21:15	10.2	3.9	N
10/3/2017 18:30	7.9	6.5	N	10/4/2017 8:00	6.7	7.4	Y	10/4/2017 21:30	9.5	3.5	N
10/3/2017 18:45	8.5	5.9	N	10/4/2017 8:15	7.3	6.1	N	10/4/2017 21:45	8.9	3.6	N
10/3/2017 19:00	7.9	6	N	10/4/2017 8:30	7.2	4.6	N	10/4/2017 22:00	8.6	2.9	N
10/3/2017 19:15	7.4	6.3	N	10/4/2017 8:45	6.6	9	Y	10/4/2017 22:15	8.7	3.6	N
10/3/2017 19:30	7.4	4.3	N	10/4/2017 9:00	9.2	14.1	Y	10/4/2017 22:30	8.4	6.3	N
10/3/2017 19:45	8.3	4.6	N	10/4/2017 9:15	7.9	4.8	N	10/4/2017 22:45	7.3	3.3	N
10/3/2017 20:00	8.9	5.2	N	10/4/2017 9:30	9.3	4.6	N	10/4/2017 23:00	7.4	3.8	N
10/3/2017 20:15	8.6	4.5	N	10/4/2017 9:45	7.6	5.1	N	10/4/2017 23:15	7.1	4.5	N
10/3/2017 20:30	8	4.9	N	10/4/2017 10:00	8.1	3.9	N	10/4/2017 23:30	7	3.8	N
10/3/2017 20:45	10.6	4.3	N	10/4/2017 10:15	7.8	3.1	N	10/4/2017 23:45	8.3	5.3	N
10/3/2017 21:00	11.1	4.6	N	10/4/2017 10:30	7.3	4.5	N	10/5/2017 0:00	7.7	6.2	N
10/3/2017 21:15	9.8	4.7	N	10/4/2017 10:45	7.5	3.9	N	10/5/2017 0:15	7.8	5.1	N
10/3/2017 21:30	8.8	4.6	N	10/4/2017 11:00	7.6	9	Y	10/5/2017 0:30	7.2	5.7	N
10/3/2017 21:45	9	4.7	N	10/4/2017 11:15	6.5	16.7	Y	10/5/2017 0:45	7	5.4	N
10/3/2017 22:00	8.3	4.8	N	10/4/2017 11:30	7.4	6	N	10/5/2017 1:00	7.5	4.9	N
10/3/2017 22:15	7.3	6.1	N	10/4/2017 11:45	6.8	5.3	N	10/5/2017 1:15	7	8.2	Y
10/3/2017 22:30	7	4.7	N	10/4/2017 12:00	7.7	5.1	N	10/5/2017 1:30	8.1	4.9	N
10/3/2017 22:45	6.6	5.3	N	10/4/2017 12:15	6.6	6.1	N	10/5/2017 1:45	9.1	6.5	N
10/3/2017 23:00	7.1	6.1	N	10/4/2017 12:30	7.6	4	N	10/5/2017 2:00	9.2	5.2	N
10/3/2017 23:15	6.5	6	N	10/4/2017 12:45	7.7	3.9	N	10/5/2017 2:15	8.5	3.7	N
10/3/2017 23:30	6.6	6.9	Y	10/4/2017 13:00	8.3	4.8	N	10/5/2017 2:30	10.2	5.2	N
10/3/2017 23:45	7.2	5.2	N	10/4/2017 13:15	8.5	3.9	N	10/5/2017 2:45	10.1	4.2	N
10/4/2017 0:00	6.8	6.3	N	10/4/2017 13:30	9.2	5.5	N	10/5/2017 3:00	10.3	4.9	N
10/4/2017 0:15	7.2	5.6	N	10/4/2017 13:45	9.4	4.5	N	10/5/2017 3:15	9	6.3	N
10/4/2017 0:30	7.4	6.4	N	10/4/2017 14:00	11.1	3.1	N	10/5/2017 3:30	9.2	4.5	N
10/4/2017 0:45	7.1	5	N	10/4/2017 14:15	10	2.5	N	10/5/2017 3:45	8.4	4.1	N
10/4/2017 1:00	7.1	4.3	N	10/4/2017 14:30	9.8	2	N	10/5/2017 4:00	7.4	4.4	N
10/4/2017 1:15	8.3	4.6	N	10/4/2017 14:45	9.7	2.1	N	10/5/2017 4:15	7.3	4.4	N
10/4/2017 1:30	9	5.1	N	10/4/2017 15:00	9.3	2.4	N	10/5/2017 4:30	6.4	4.6	N
10/4/2017 1:45	7.9	4.5	N	10/4/2017 15:15	8.5	2.1	N	10/5/2017 4:45	6.2	5.1	N
10/4/2017 2:00	9.1	4	N	10/4/2017 15:30	8.5	1.8	N	10/5/2017 5:00	5.3	5.2	N
10/4/2017 2:15	7	5.3	N	10/4/2017 15:45	7.2	1.8	N	10/5/2017 5:15	5.3	5.3	N
10/4/2017 2:30	7.2	5.5	N	10/4/2017 16:00	7.3	1.6	N	10/5/2017 5:30	4.8	5	Y
10/4/2017 2:45	6.6	4.8	N	10/4/2017 16:15	6.4	1.8	N	10/5/2017 5:45	5.7	5	N
10/4/2017 3:00	6.6	5.7	N	10/4/2017 16:30	7	1.6	N	10/5/2017 6:00	5.6	4.8	N
10/4/2017 3:15	6.2	5.1	N	10/4/2017 16:45	7.5	2.6	N	10/5/2017 6:15	5.4	4.9	N
10/4/2017 3:30	5.9	4.7	N	10/4/2017 17:00	6.4	2.7	N	10/5/2017 6:30	6.1	5.7	N
10/4/2017 3:45	5.5	5.9	N	10/4/2017 17:15	6.5	2	N	10/5/2017 6:45	5.9	6.4	Y
10/4/2017 4:00	4.9	6.4	Y	10/4/2017 17:30	6.7	2.3	N	10/5/2017 7:00	6.1	7.8	Y
10/4/2017 4:15	5.1	7	Y	10/4/2017 17:45	6.6	2.1	N				
Average	7.5	6.0	N								
Maximum	11.1	16.7	Y								

**TRC WEEKLY COMMUNITY AIR MONITORING PROJECT REPORT**





**Gowanus Canal TB-4 Dredging and Pilot Study  
Brooklyn, New York  
Weekly Report  
(TRC Project No.274286-0000-00000)**

**Community Air Monitoring Project  
9<sup>th</sup> Weekly Monitoring Period  
Summary Report:  
November 27<sup>th</sup> through December 1<sup>st</sup>, 2017**

**Report Contents**

- Executive Summary
- Daily Data Summary Report – PM<sub>10</sub>/TVOC
  - Daily Meteorological Summary Report
    - Periodic Monitoring Results

# Gowanus Canal TB-4 Dredging and Pilot Study Brooklyn, New York

## Executive Summary – Week 9 Monitoring Period November 27<sup>th</sup> through December 1<sup>st</sup>, 2017

The following report summarizes site air monitoring activities for the Week 6 monitoring period from November 27<sup>th</sup> through December 1<sup>st</sup>, 2017. The start and stop times associated with each daily monitoring period are listed on the respective daily reports.

TRC continued to operate two (2) air monitoring stations on the Citizen Property or Staging Area, and five (5) air monitoring stations in the 4<sup>th</sup> St Turning Basin Area using the equipment specified previously in the *Gowanus Canal TB-4 Dredging and Pilot Study Executive Summary – Background Monitoring Period Report*. During the Week 9 monitoring period there were no PM<sub>10</sub> or TVOC exceedances of the action level of 150ug/m<sup>3</sup> or 1,000 ppb respectively as defined in the *Community Air Monitoring Plan for the Gowanus Canal TB-4 Dredging and Pilot Study Project Brooklyn, NY, August 2017*.

Figure 1 depicts Total Volatile Organics (TVOC) daily averages and maximums. Figure 2 depicts particulate monitoring (PM<sub>10</sub>) daily averages and maximums for Week 9.

Additional monitoring for hydrogen sulfide, ammonia, and formaldehyde took place at all stations throughout the Week 9 monitoring period twice daily. The results of these measurements are shown in Table 1.

During the Week 9 monitoring period of November 30<sup>th</sup>, through December 1<sup>st</sup>, 2017, TRC conducted Volatile Organic Compounds (USEPA Method TO-15) sampling at Station 1 and 6. ST-1 was collected on November 29<sup>th</sup>, through November 30<sup>th</sup>, 2017. Collocated samples were collected at Station 6 (ST-6A and ST-6B) on November 30<sup>th</sup>, through December 1<sup>st</sup>, 2017. All samples were collected over a 24 hour period. Samples were shipped to Con-Test Analytical Laboratory for analyses. The results of the summa canister sampling are pending lab analyses.

Site activities were conducted at the Citizen Property on November 27<sup>th</sup> through December 1<sup>st</sup>, 2017 which included the following:

- Material and equipment deliveries on Citizen Property
- General vehicular traffic site-wide throughout the monitoring period
- Maintenance of the barges and equipment

Site activities were conducted at the 4<sup>th</sup> St Turning Basin Area of the Canal on November 27<sup>th</sup> through December 1<sup>st</sup>, 2017 which included the following:

- Installation of 18 pairs of Sheet Piling on the north side of the canal near Whole Foods
- Probing to determine edge of toe of existing bulkhead near Whole Foods
- Installation of false work (i.e., vertical and horizontal alignment guide) in preparation for Sheet Piling

# Gowanus Canal TB-4 Dredging and Capping Pilot Study

## Brooklyn, New York

Daily Station Report – TVOC/PM<sub>10</sub>  
(TRC Project No.274286-0000-00000)

11/27/2017 06:30 AM - 11/27/17 23:45 PM

### Station 1

TVOC			PM <sub>10</sub>		
Max.	37	ppb	Max.	14	ug/m <sup>3</sup>
Avg.	2	ppb	Avg.	6	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 2

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	12	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	6	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 3

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	6	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 4

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	19	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	6	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 5

TVOC			PM <sub>10</sub>		
Max.	9	ppb	Max.	12	ug/m <sup>3</sup>
Avg.	1	ppb	Avg.	6	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 6

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	12	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	5	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 7

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

TVOC – Total Volatile Organic Compounds

PM<sub>10</sub> – Particulates as PM<sub>10</sub>

Max. – Maximum daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Avg. – Daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Exc. – Total # of averages which exceed the action level (≥1 ppm - TVOC / ≥150 ug/m<sup>3</sup> - PM<sub>10</sub>)

# Gowanus Canal TB-4 Dredging and Capping Pilot Study

## Brooklyn, New York

Daily Station Report – TVOC/PM<sub>10</sub>  
(TRC Project No.274286-0000-00000)

11/28/2017 00:00 AM - 11/28/17 23:45 PM

### Station 1

TVOC			PM <sub>10</sub>		
Max.	2	ppb	Max.	26	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	7	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 2

TVOC			PM <sub>10</sub>		
Max.	5	ppb	Max.	79	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	9	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 3

TVOC			PM <sub>10</sub>		
Max.	135	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	28	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 4

TVOC			PM <sub>10</sub>		
Max.	38	ppb	Max.	21	ug/m <sup>3</sup>
Avg.	2	ppb	Avg.	7	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 5

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	19	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	7	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 6

TVOC			PM <sub>10</sub>		
Max.	47	ppb	Max.	14	ug/m <sup>3</sup>
Avg.	37	ppb	Avg.	7	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 7

TVOC			PM <sub>10</sub>		
Max.	108	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	71	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

TVOC – Total Volatile Organic Compounds

PM<sub>10</sub> – Particulates as PM<sub>10</sub>

Max. – Maximum daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Avg. – Daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Exc. – Total # of averages which exceed the action level (≥1 ppm - TVOC / ≥150 ug/m<sup>3</sup> - PM<sub>10</sub>)

# Gowanus Canal TB-4 Dredging and Capping Pilot Study

## Brooklyn, New York

Daily Station Report – TVOC/PM<sub>10</sub>  
(TRC Project No.274286-0000-00000)

11/29/2017 00:00 AM - 11/29/17 23:45 PM

### Station 1

TVOC			PM <sub>10</sub>		
Max.	85	ppb	Max.	18	ug/m <sup>3</sup>
Avg.	6	ppb	Avg.	8	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 2

TVOC			PM <sub>10</sub>		
Max.	3	ppb	Max.	21	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	9	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 3

TVOC			PM <sub>10</sub>		
Max.	27	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	3	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 4

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	16	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	2	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 5

TVOC			PM <sub>10</sub>		
Max.	7	ppb	Max.	8	ug/m <sup>3</sup>
Avg.	6	ppb	Avg.	5	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 6

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	6	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	2	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 7

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

TVOC – Total Volatile Organic Compounds

PM<sub>10</sub> – Particulates as PM<sub>10</sub>

Max. – Maximum daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Avg. – Daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Exc. – Total # of averages which exceed the action level (≥1 ppm - TVOC / ≥150 ug/m<sup>3</sup> - PM<sub>10</sub>)

# Gowanus Canal TB-4 Dredging and Capping Pilot Study

## Brooklyn, New York

Daily Station Report – TVOC/PM<sub>10</sub>  
(TRC Project No.274286-0000-00000)

11/30/2017 00:00 AM - 11/30/17 23:45 PM

### Station 1

TVOC			PM <sub>10</sub>		
Max.	5	ppb	Max.	29	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	7	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 2

TVOC			PM <sub>10</sub>		
Max.	30	ppb	Max.	38	ug/m <sup>3</sup>
Avg.	1	ppb	Avg.	8	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 3

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 4

TVOC			PM <sub>10</sub>		
Max.	2	ppb	Max.	19	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	7	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 5

TVOC			PM <sub>10</sub>		
Max.	61	ppb	Max.	11	ug/m <sup>3</sup>
Avg.	16	ppb	Avg.	4	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 6

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	2	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 7

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

TVOC – Total Volatile Organic Compounds

PM<sub>10</sub> – Particulates as PM<sub>10</sub>

Max. – Maximum daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Avg. – Daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Exc. – Total # of averages which exceed the action level (≥1 ppm - TVOC / ≥150 ug/m<sup>3</sup> - PM<sub>10</sub>)

# Gowanus Canal TB-4 Dredging and Capping Pilot Study

## Brooklyn, New York

Daily Station Report – TVOC/PM<sub>10</sub>  
(TRC Project No.274286-0000-00000)

12/01/2017 00:00 AM - 12/01/17 15:00 PM

### Station 1

TVOC			PM <sub>10</sub>		
Max.	1	ppb	Max.	20	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	10	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 2

TVOC			PM <sub>10</sub>		
Max.	2	ppb	Max.	17	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	10	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 3

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 4

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	18	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	5	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 5

TVOC			PM <sub>10</sub>		
Max.	7	ppb	Max.	8	ug/m <sup>3</sup>
Avg.	2	ppb	Avg.	2	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 6

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	9	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

### Station 7

TVOC			PM <sub>10</sub>		
Max.	<1	ppb	Max.	<1	ug/m <sup>3</sup>
Avg.	<1	ppb	Avg.	<1	ug/m <sup>3</sup>
Exc.	0	total	Exc.	0	Total

TVOC – Total Volatile Organic Compounds



PM<sub>10</sub> – Particulates as PM<sub>10</sub>

Max. – Maximum daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)



Avg. – Daily average (15 min. avg. – TVOC / 15 min. avg. – PM<sub>10</sub>)

Exc. – Total # of averages which exceed the action level (≥1 ppm - TVOC / ≥150 ug/m<sup>3</sup> - PM<sub>10</sub>)

**Figure 1**  
**Gowanus Canal Superfund Site -TB4 Dredging and Capping Pilot Program**  
**TVOC Monitoring Data - Week 9**

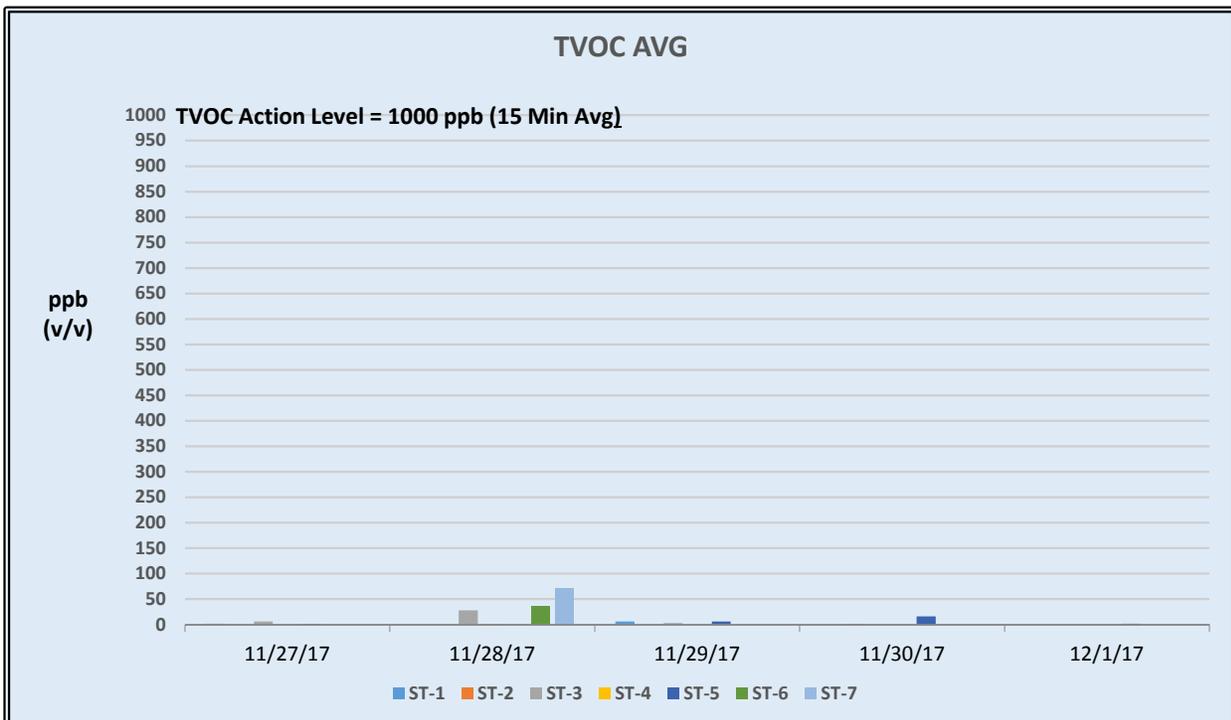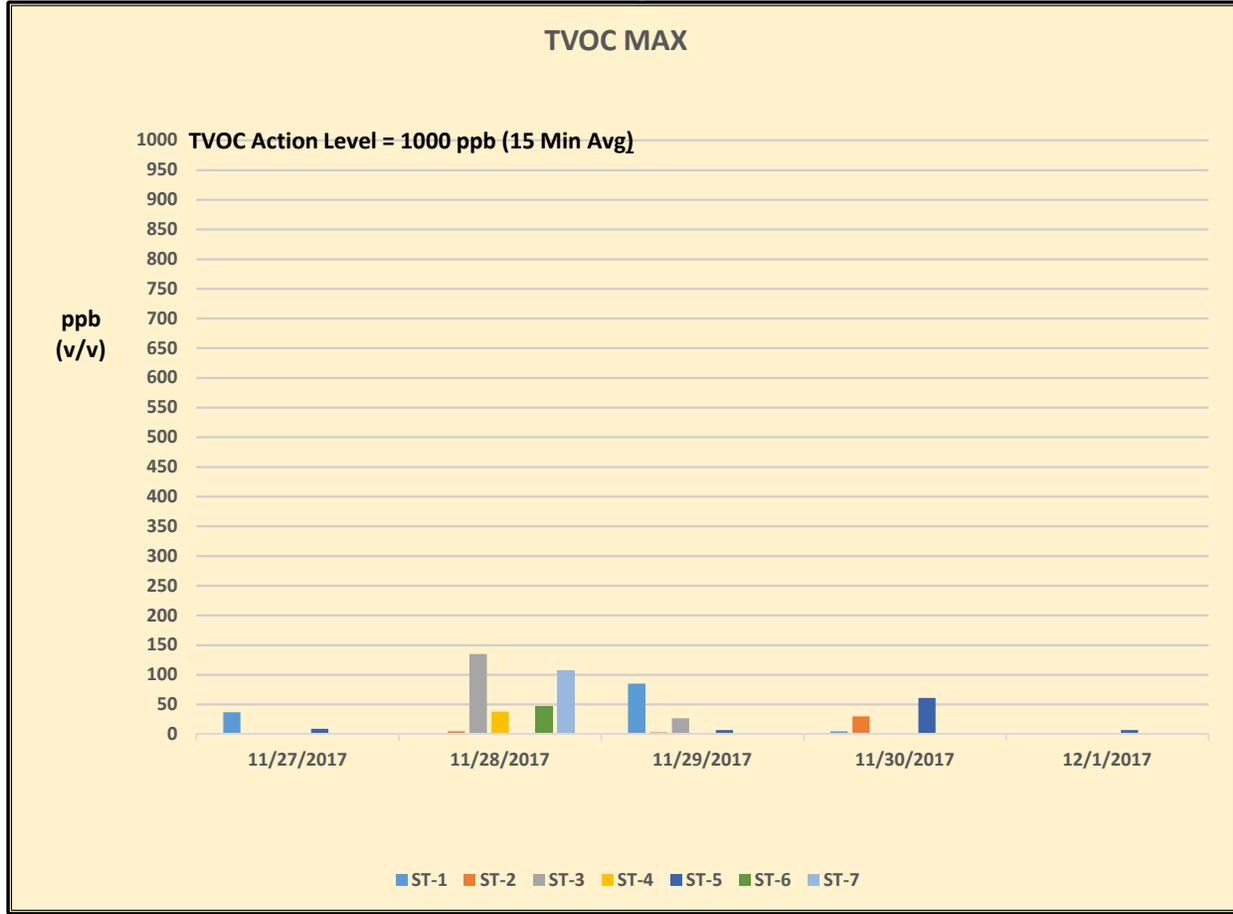

**Figure 2**  
**Gowanus Canal Superfund Site - TB4 Dredging and Capping Pilot Program**  
**TRC CAMP PM<sub>10</sub> Monitoring Data - Week 9**

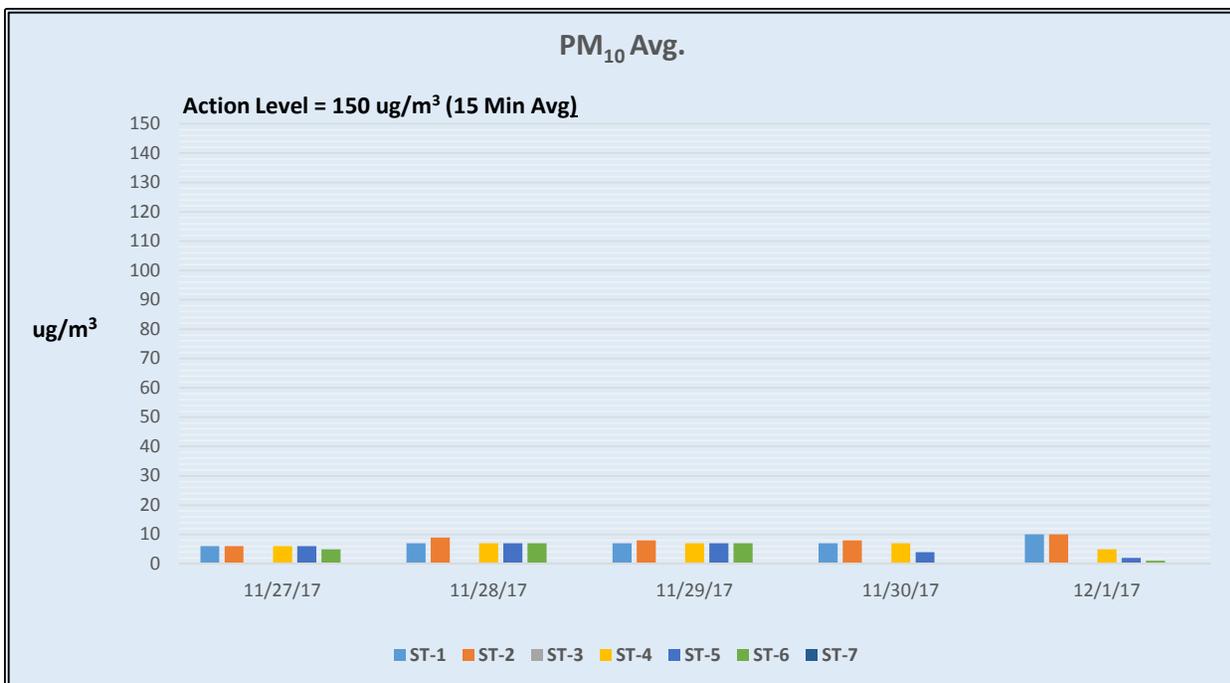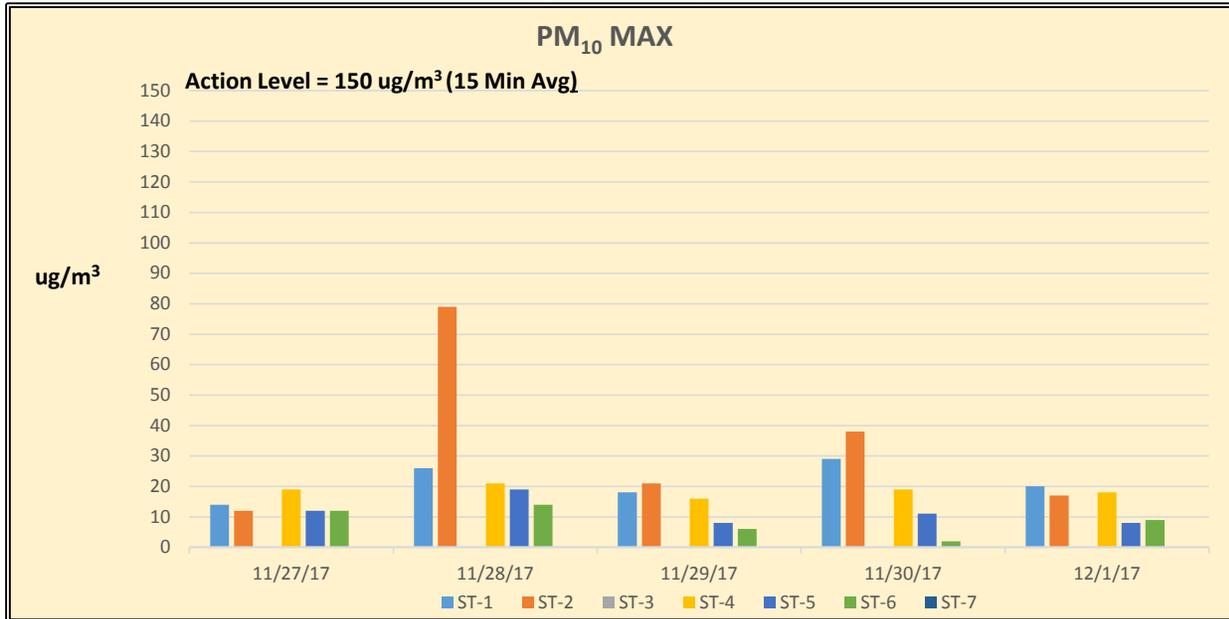

**Table 1****Week 9****Summary of Additional Periodic (Daily) Monitoring Data**

November 27 <sup>th</sup> , 2017				
Station Id	Time	Formaldehyde (CHO) (ppb)	Hydrogen Sulfide (H <sub>2</sub> S) (ppb)	Ammonia (NH <sub>3</sub> ) (ppm)
ST-1	7:00	<50	<3	<1
	14:10	<50	<3	<1
ST-2	7:05	<50	<3	<1
	14:15	<50	<3	<1
ST-3	7:15	<50	<3	<1
	14:35	<50	<3	<1
ST-4	7:20	<50	<3	<1
	14:40	<50	<3	<1
ST-5	7:25	<50	<3	<1
	14:45	<50	<3	<1
ST-6	7:40	<50	<3	<1
	14:55	<50	<3	<1
ST-7	7:55	<50	<3	<1
	15:00	<50	<3	<1

November 28 <sup>th</sup> , 2017				
Station Id	Time	Formaldehyde (CHO) (ppb)	Hydrogen Sulfide (H <sub>2</sub> S) (ppb)	Ammonia (NH <sub>3</sub> ) (ppm)
ST-1	7:30	<50	<3	<1
	14:30	<50	<3	<1
ST-2	7:35	<50	<3	<1
	14:35	<50	<3	<1
ST-3	7:50	<50	<3	<1
	14:50	<50	<3	<1
ST-4	8:00	<50	<3	<1
	14:55	<50	<3	<1
ST-5	8:05	<50	<3	<1
	15:00	<50	<3	<1
ST-6	8:30	<50	<3	<1
	15:30	<50	<3	<1
ST-7	8:50	<50	<3	<1
	15:15	<50	<3	<1

**Table 1****Week 9****Summary of Additional Periodic (Daily) Monitoring Data**

November 29 <sup>th</sup> , 2017				
Station Id	Time	Formaldehyde (CHO) (ppb)	Hydrogen Sulfide (H <sub>2</sub> S) (ppb)	Ammonia (NH <sub>3</sub> ) (ppm)
ST-1	6:30	<50	<3	<1
	13:10	<50	<3	<1
ST-2	6:35	<50	<3	<1
	13:15	<50	<3	<1
ST-3	6:45	<50	<3	<1
	13:25	<50	<3	<1
ST-4	6:50	<50	<3	<1
	13:30	<50	<3	<1
ST-5	6:55	<50	<3	<1
	13:35	<50	<3	<1
ST-6	7:10	<50	<3	<1
	13:50	<50	<3	<1
ST-7	7:20	<50	<3	<1
	13:45	<50	<3	<1

November 30 <sup>th</sup> , 2017				
Station Id	Time	Formaldehyde (CHO) (ppb)	Hydrogen Sulfide (H <sub>2</sub> S) (ppb)	Ammonia (NH <sub>3</sub> ) (ppm)
ST-1	7:45	<50	<3	<1
	13:30	<50	<3	<1
ST-2	7:50	<50	<3	<1
	13:35	<50	<3	<1
ST-3	8:40	<50	<3	<1
	14:00	<50	<3	<1
ST-4	8:15	<50	<3	<1
	14:05	<50	<3	<1
ST-5	8:20	<50	<3	<1
	14:10	<50	<3	<1
ST-6	8:40	<50	<3	<1
	14:30	<50	<3	<1
ST-7	9:00	<50	<3	<1
	14:25	<50	<3	<1

**Table 1**

**Week 9**

**Summary of Additional Periodic (Daily) Monitoring Data**

December 1 <sup>st</sup> , 2017				
Station Id	Time	Formaldehyde (CHO) (ppb)	Hydrogen Sulfide (H <sub>2</sub> S) (ppb)	Ammonia (NH <sub>3</sub> ) (ppm)
ST-1	8:00	<50	<3	<1
	12:15	<50	<3	<1
ST-2	8:05	<50	<3	<1
	12:20	<50	<3	<1
ST-3	8:20	<50	<3	<1
	13:00	<50	<3	<1
ST-4	8:25	<50	<3	<1
	13:05	<50	<3	<1
ST-5	8:30	<50	<3	<1
	13:10	<50	<3	<1
ST-6	8:50	<50	<3	<1
	13:30	<50	<3	<1
ST-7	9:10	<50	<3	<1
	13:45	<50	<3	<1

**\*(ppb) Indicates results reported in parts per billion**

**\* (ppm) Indicates results reported in parts per million**



# Gowanus Canal TB-4 Dredging and Capping Pilot Study Brooklyn, New York

## Meteorological Summary

November 27<sup>h</sup> through December 1<sup>st</sup>, 2017

November 27 <sup>th</sup> , 2017		
Wind Direction (°)	Wind Speed (mph)	Temperature (°F)
<b>WSW</b>	<b>3.31</b>	<b>40.2</b>

November 28 <sup>th</sup> , 2017		
Wind Direction (°)	Wind Speed (mph)	Temperature (°F)
<b>E</b>	<b>4.43</b>	<b>44.8</b>

November 29 <sup>th</sup> , 2017		
Wind Direction (°)	Wind Speed (mph)	Temperature (°F)
<b>ENE</b>	<b>4.04</b>	<b>45.4</b>

November 30 <sup>th</sup> , 2017		
Wind Direction (°)	Wind Speed (mph)	Temperature (°F)
<b>SE</b>	<b>4.20</b>	<b>42.6</b>

December 1 <sup>st</sup> , 2017		
Wind Direction (°)	Wind Speed (mph)	Temperature (°F)
<b>W</b>	<b>2.58</b>	<b>49.2</b>

\*All meteorological data represents an average for the time period of 06:30 to 23:45 for Monday.

\*All meteorological data represents averages for the time period of 00:00 to 23:45 for Tuesday.

\*All meteorological data represents an average for the time period of 00:00 to 15:00 for Friday.

**WILSON IHRIG WEEKLY NOISE AND VIBRATION MONITORING REPORT**





WI #15-081

**MEMORANDUM**

December 4, 2017

To: William Lee/ de maximis, inc.  
Kirsten Meyers / TRC

From: Silas Bensing, Ani Toncheva / Wilson Ihrig

Subject: Gowanus Canal 4th Street Turning Basin Dredging and Capping Pilot Study, Weekly Noise and Vibration Monitoring Report, 27 November – 01 December, 2017

**Noise Monitoring Locations**

Figure 1 shows the noise monitoring locations. NM-1 is installed at a light pole on the north side of TB4 and is approximately 25 feet from the north edge of the canal. NM-2 is installed at the existing guard rail on the south side of TB4, approximately 4 feet from the south edge of the canal. NM-3 is installed at a light pole on the north side of TB4 near 3rd Avenue, approximately 50 feet from the north edge of the canal. Photos 1, 2, and 3 show the recent field conditions at the monitors.

**Vibration Monitoring Locations**

Figure 1 shows the vibration monitoring locations. Vibration monitor VM-1 is installed at the parking lot curb on the north side of TB4, approximately 45 feet from the north edge of the canal. Vibration monitor VM-2 is installed near the corner of an existing building on the south side of TB4, approximately 24 feet from the south edge of the canal. Photos 4 and 5 show the recent field conditions at the monitors.

**Noise Monitoring Results**


Figures 2 through 16 present the hourly Leq noise levels compared with the noise thresholds discussed in the noise monitoring plan<sup>1</sup>. Commercial and Industrial land uses are assigned an hourly Leq noise limit of 80 dBA for Daytime and Evening time periods. The average baseline noise measured in the project area in 2015 are also shown for reference<sup>2</sup>.

<sup>1</sup> Wilson Ihrig. *Gowanus Canal 4<sup>th</sup> Street Turning Basin Dredging and Capping Pilot Study Noise and Vibration Monitoring Plan*. California: prepared for Gowanus Canal Remedial Design Group, DRAFT May 2017

<sup>2</sup> Wilson Ihrig. *Gowanus Canal Remedial Design Project RTA-1 Noise and Vibration Baseline Report*. California: prepared for Geosyntec Consultants Inc., October 2015.

## Vibration Monitoring Results

Figures 17 through 26 present the maximum peak particle velocity (PPV) vibration events compared with the thresholds discussed in the vibration monitoring plan<sup>3</sup>. Commercial and Industrial structures are assigned a PPV vibration criterion of 2.0 inches/second

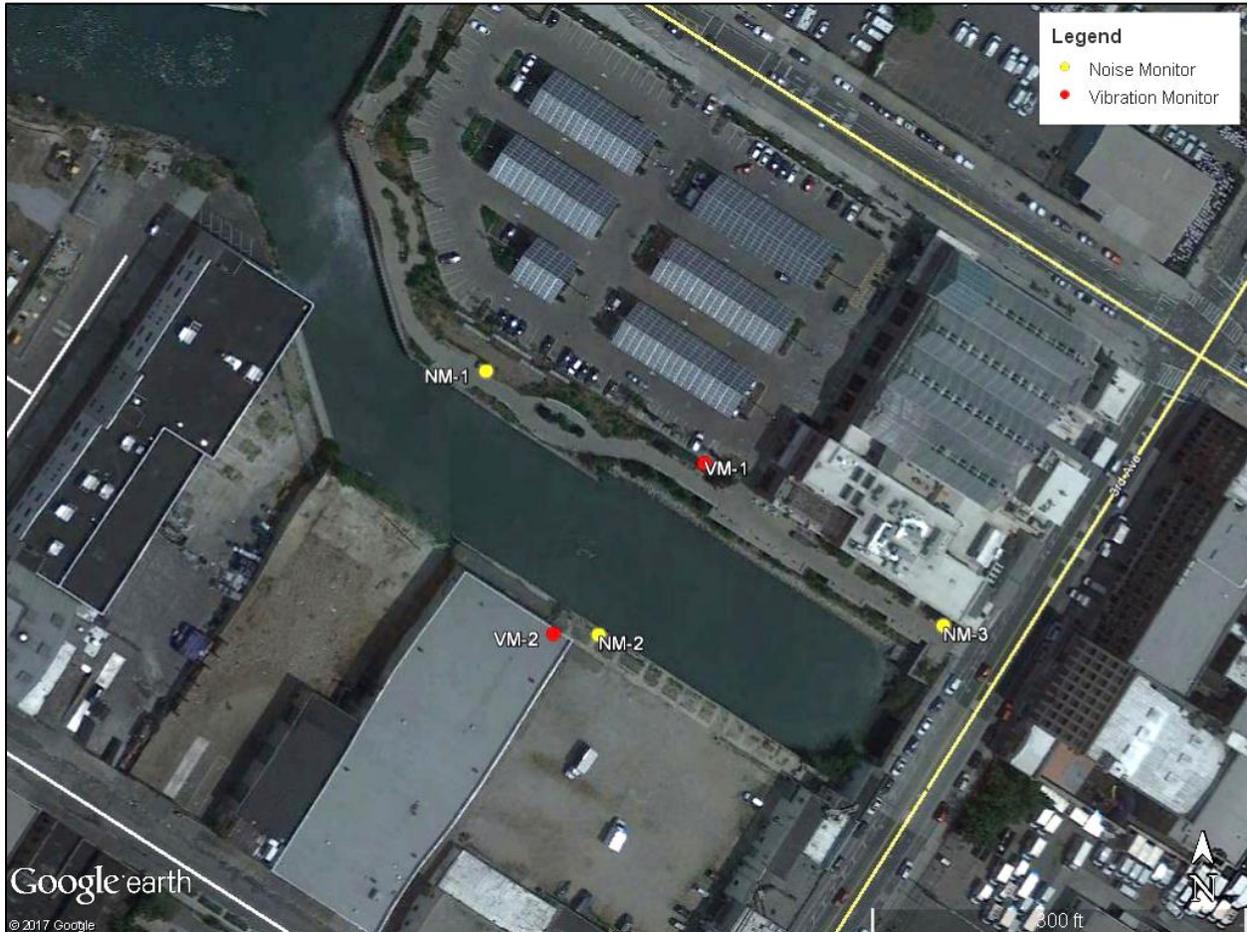

**Figure 1: Long-term Noise and Vibration Monitoring Locations for Gowanus TB4 Dredging and Capping Pilot Study**


<sup>3</sup> Wilson Ihrig. *Gowanus Canal 4<sup>th</sup> Street Turning Basin Dredging and Capping Pilot Study Noise and Vibration Monitoring Plan*. California: prepared for Gowanus Canal Remedial Design Group, DRAFT May 2017




**Photo 1: Noise Monitoring Location NM-1**  
**(26 September 2017)**



**Photo 2: Noise Monitoring Location NM-2**  
**(25 September 2017)**

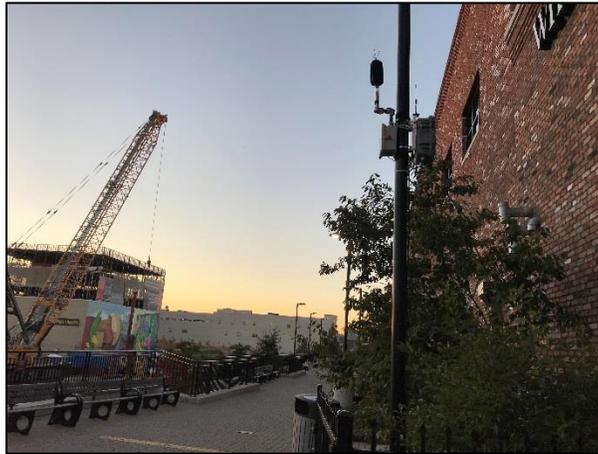


**Photo 3: Noise Monitoring Location NM-3**  
**(29 October 2017)**

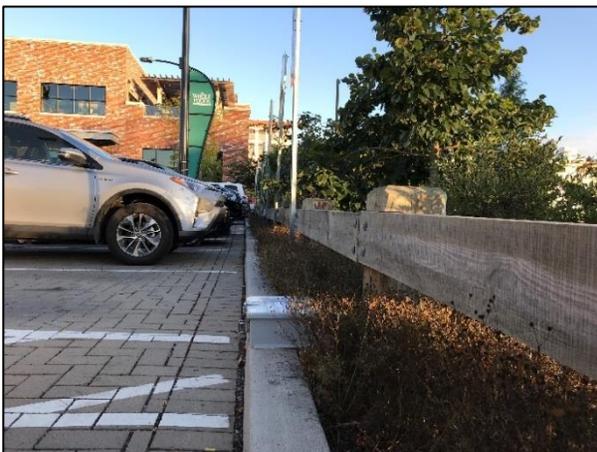

**Photo 4: Vibration Monitoring Location VM-1**  
**(12 October 2017)**




**Photo 5: Vibration Monitoring Location VM-2**  
**(12 October 2017)**

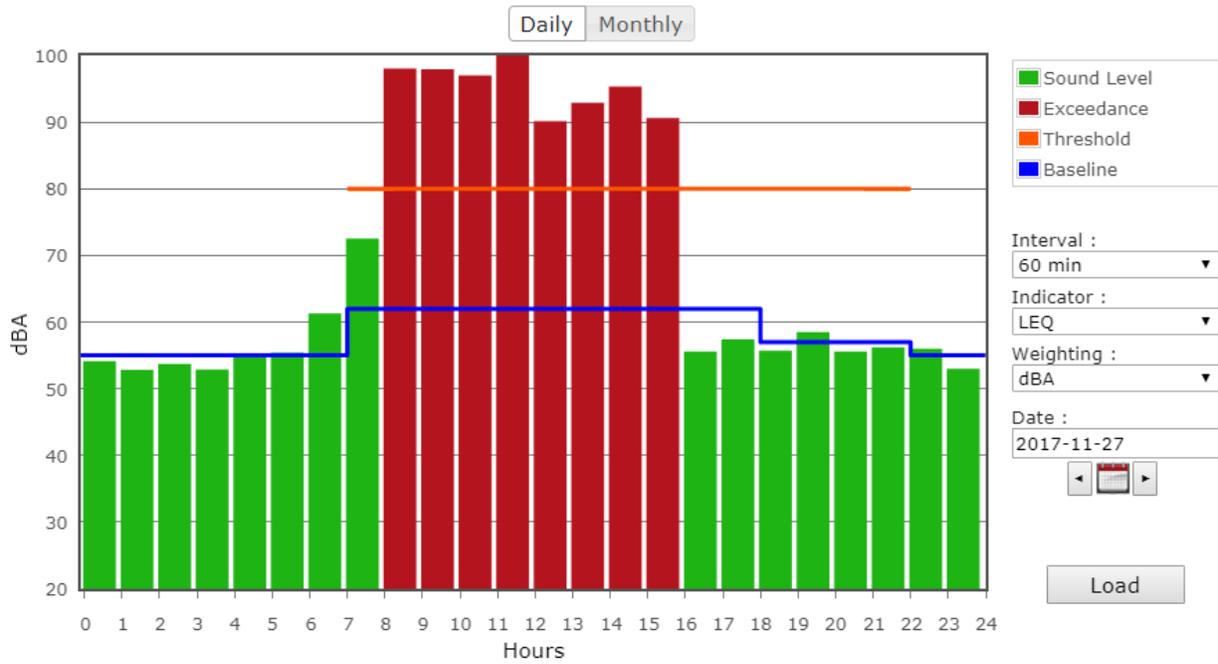

**Figure 2: North Monitor NM-1 on Monday\***

\*Noise Level for the 11:00-Noon interval was 100.1 dBA.

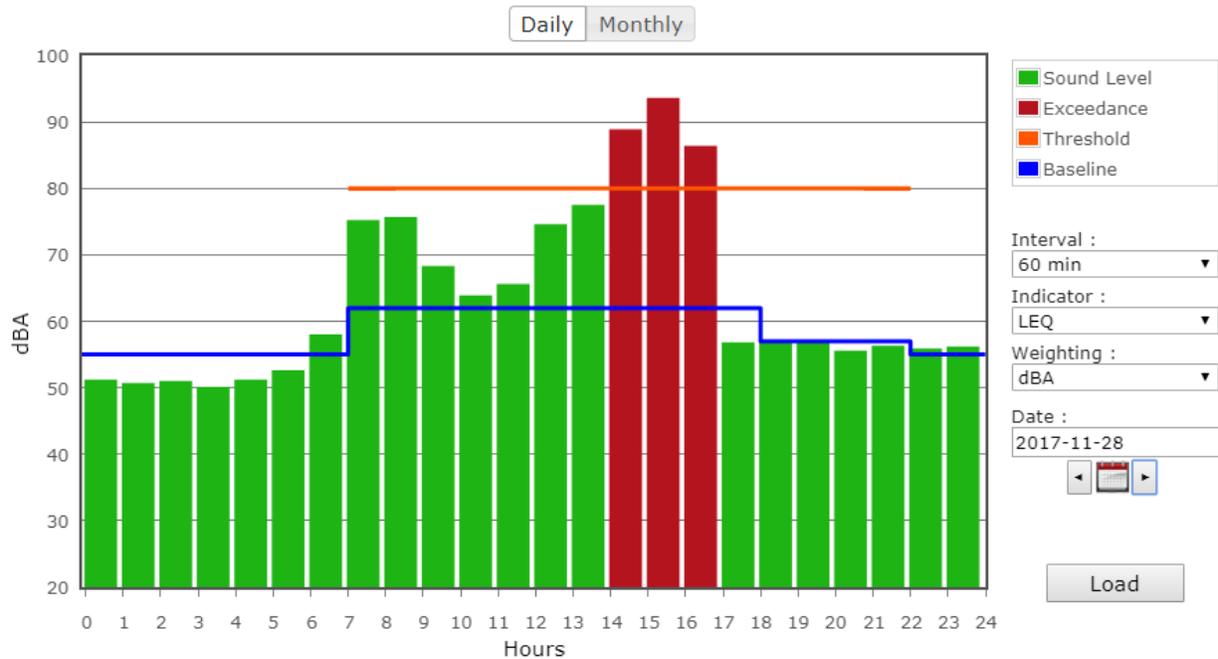

**Figure 3: North Monitor NM-1 on Tuesday**

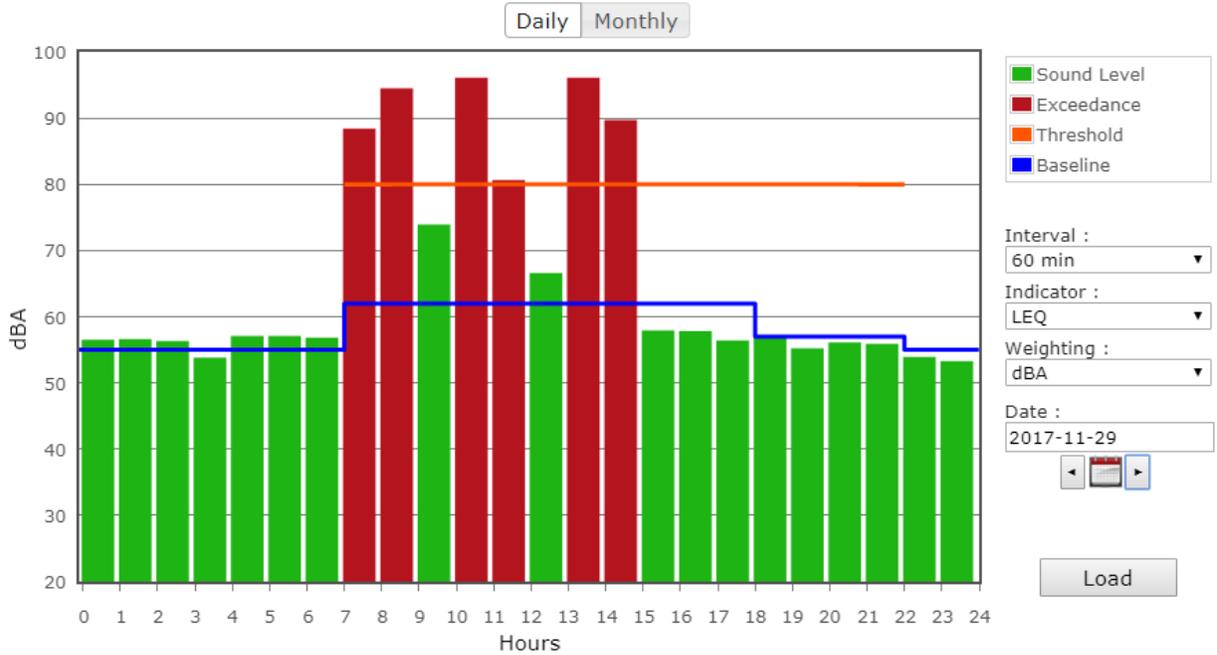


Figure 4: North Monitor NM-1 on Wednesday

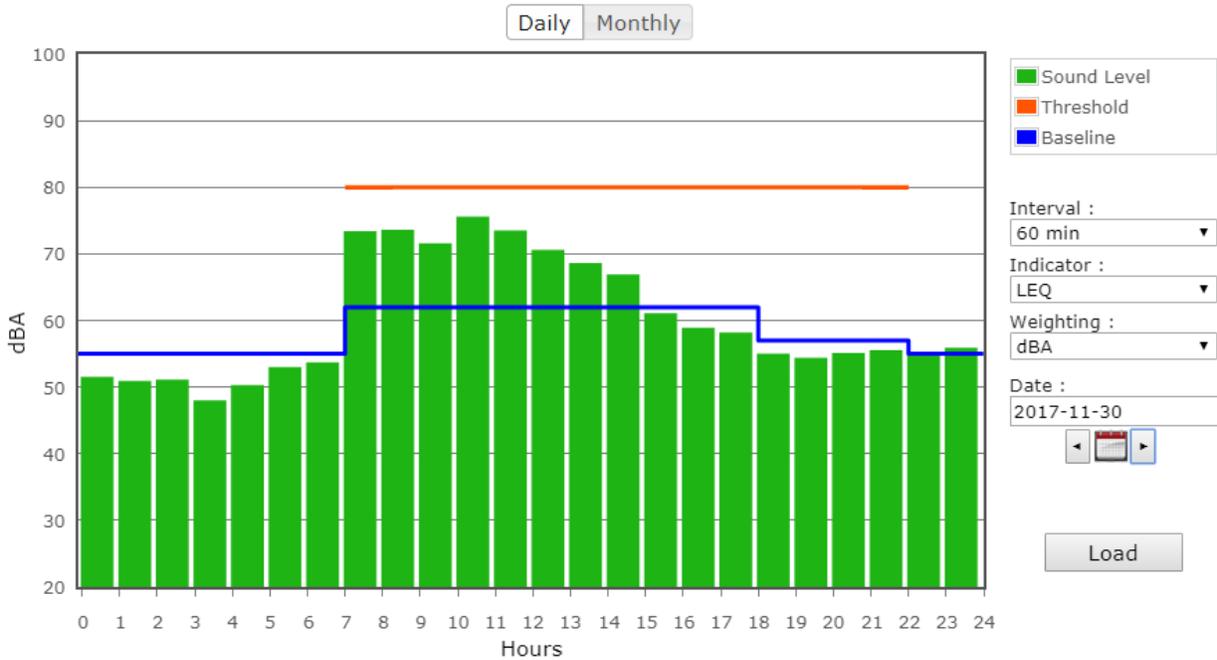


Figure 5: North Monitor NM-1 on Thursday

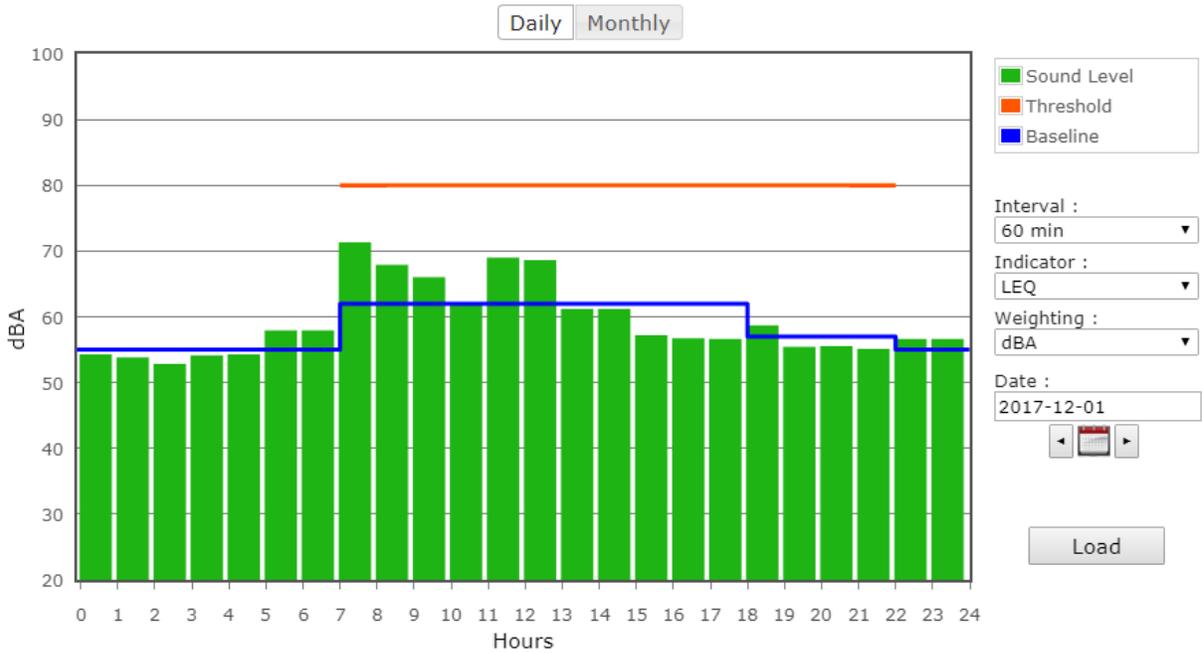


Figure 6: North Monitor NM-1 on Friday



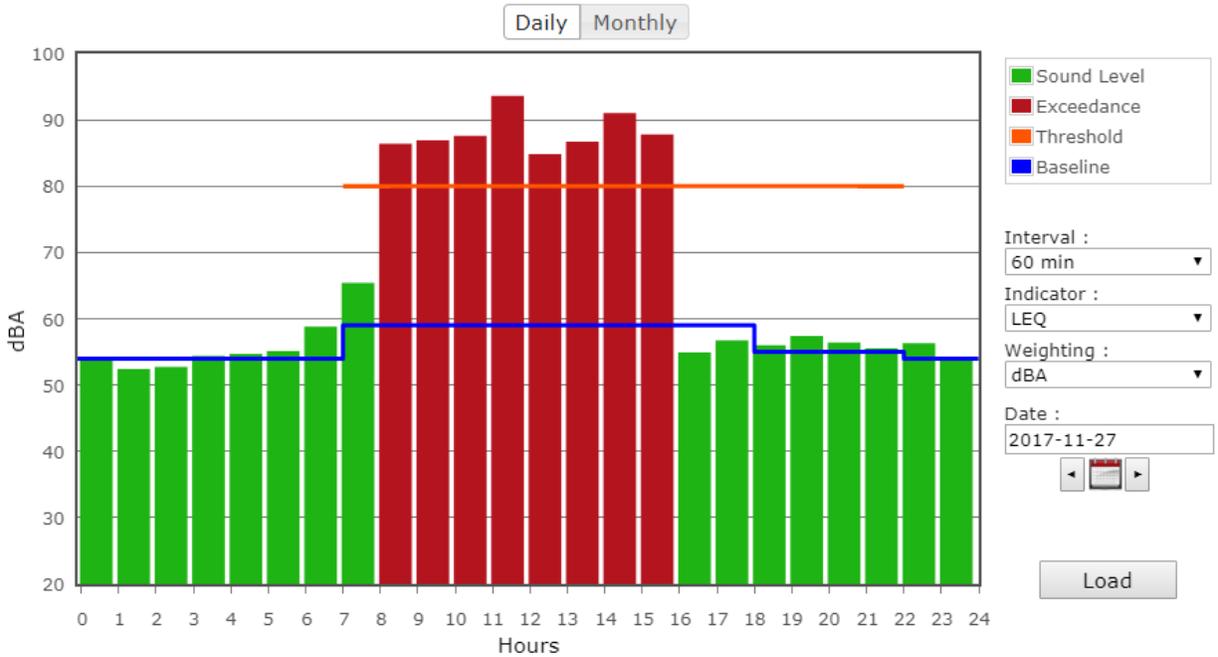


Figure 7: South Monitor NM-2 on Monday

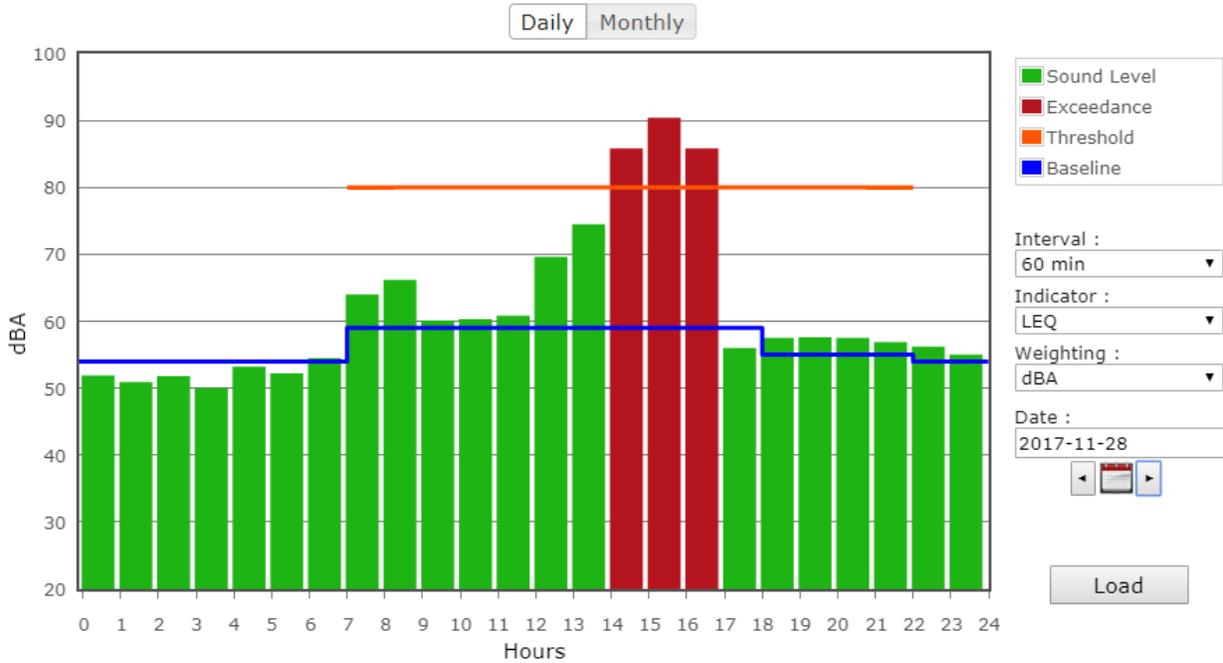

**Figure 8: South Monitor NM-2 on Tuesday**

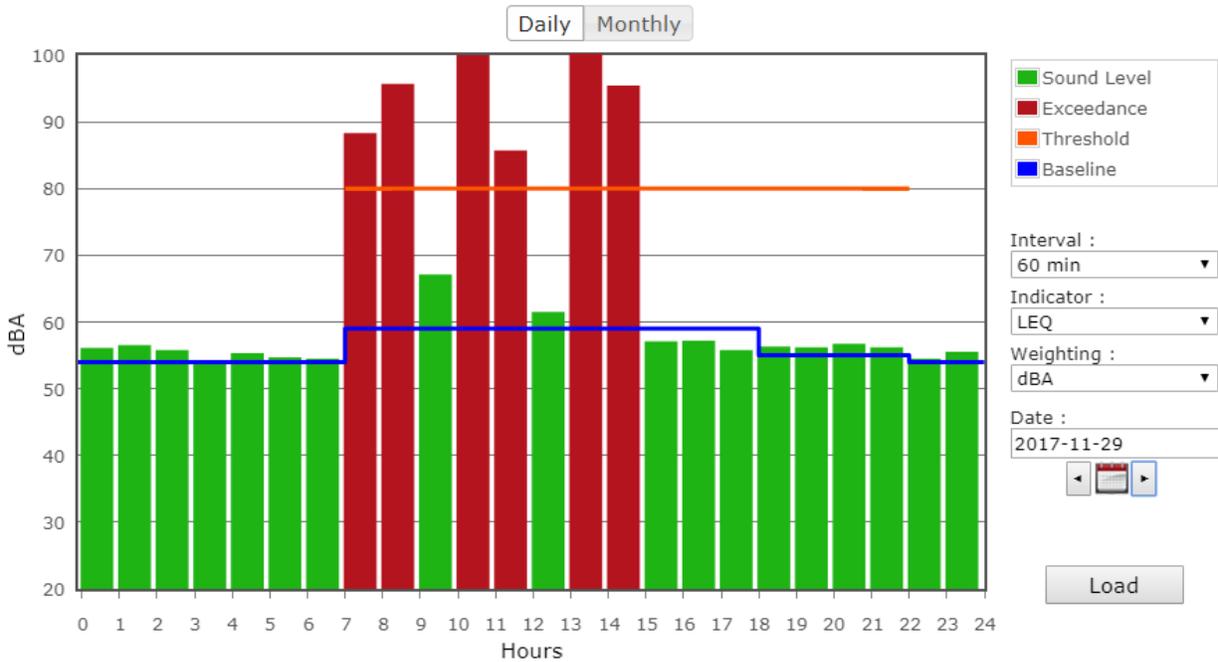

**Figure 9: South Monitor NM-2 on Wednesday\***

\*Noise Levels are 99.8 dBA at 10:00 and 100 dBA at 13:00.

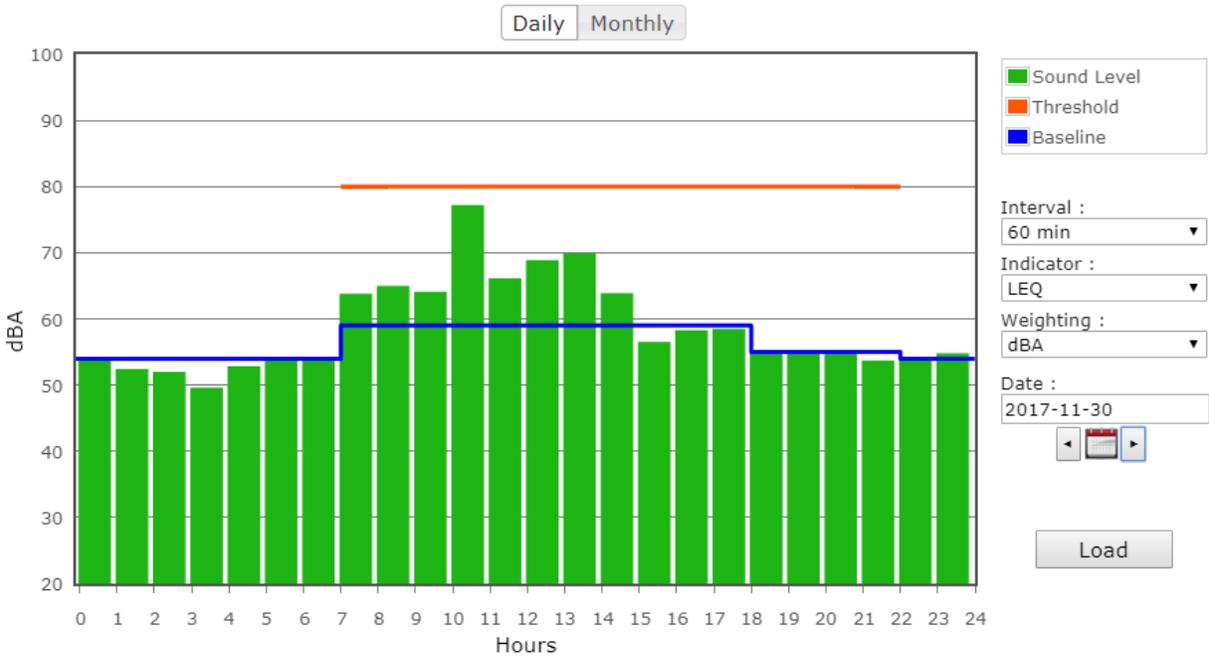


Figure 10: South Monitor NM-2 on Thursday

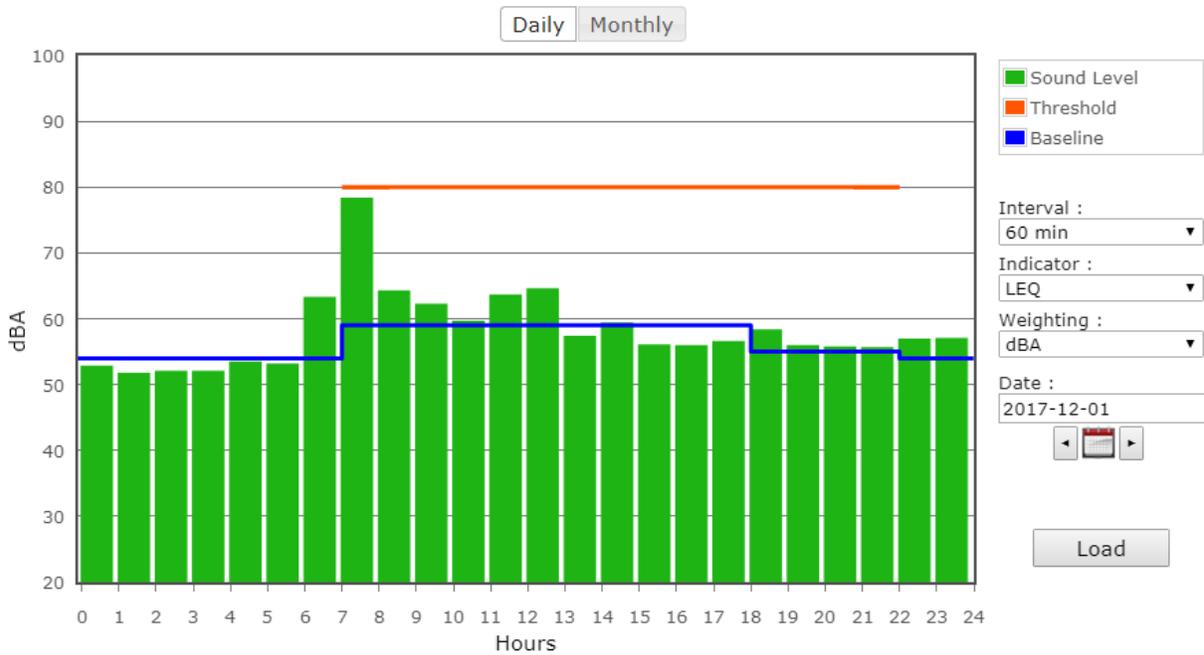


Figure 11: South Monitor NM-2 on Friday

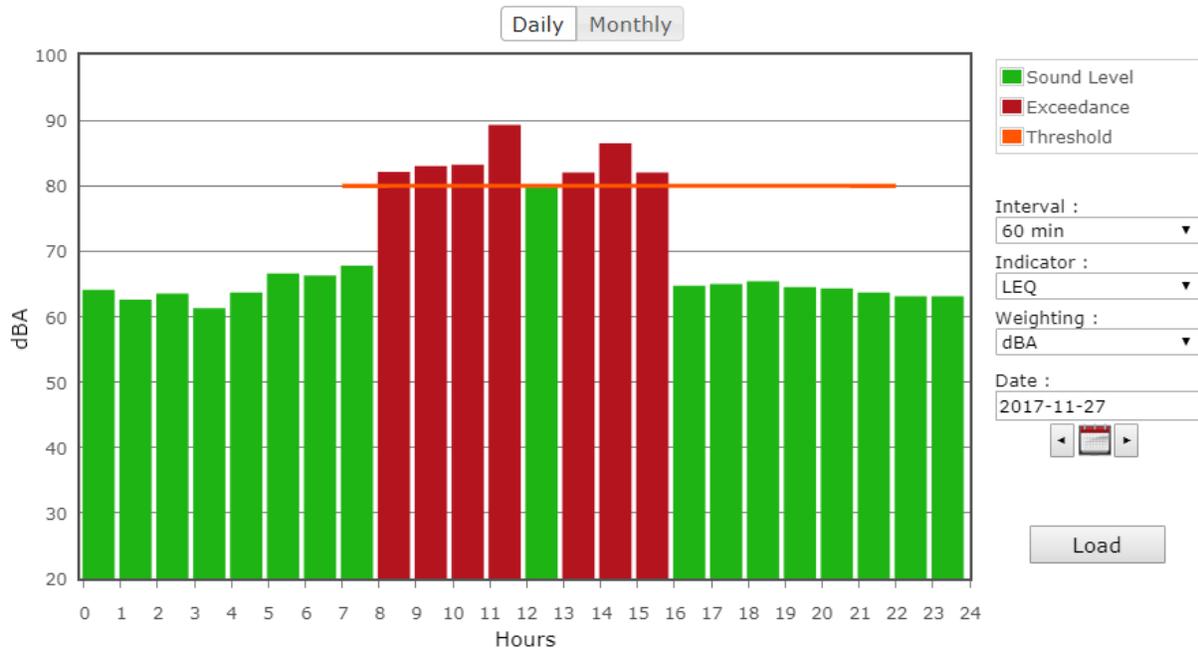


Figure 12: Northeast Monitor NM-3 on Monday



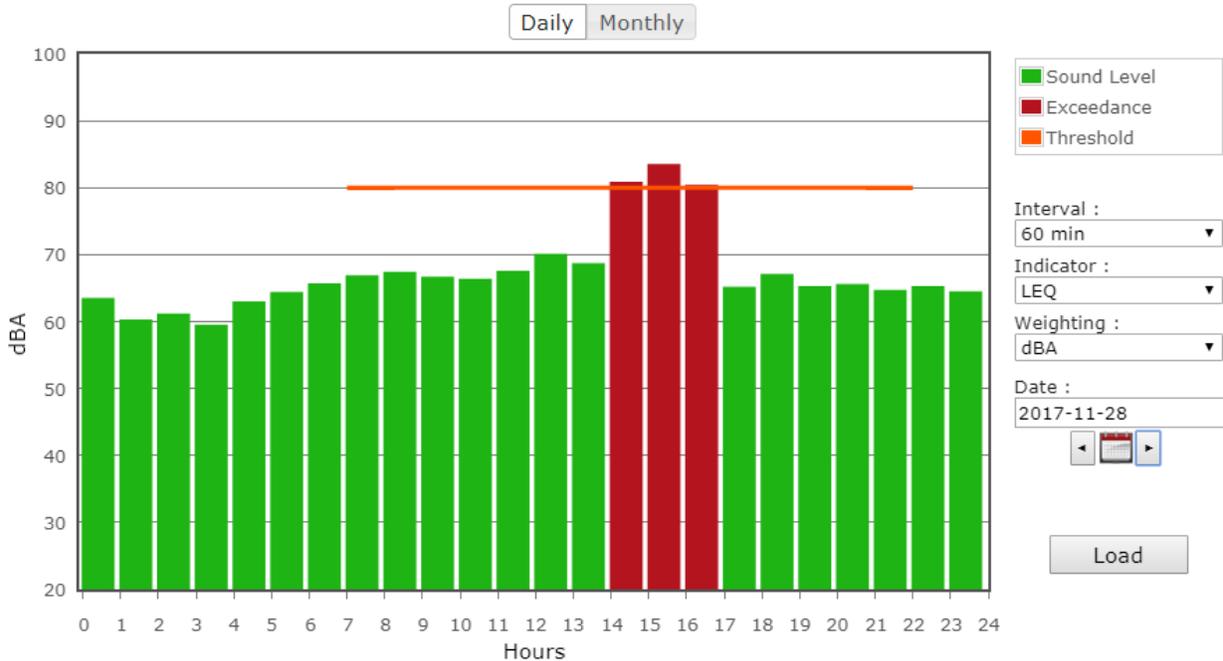



Figure 13: Northeast Monitor NM-3 on Tuesday

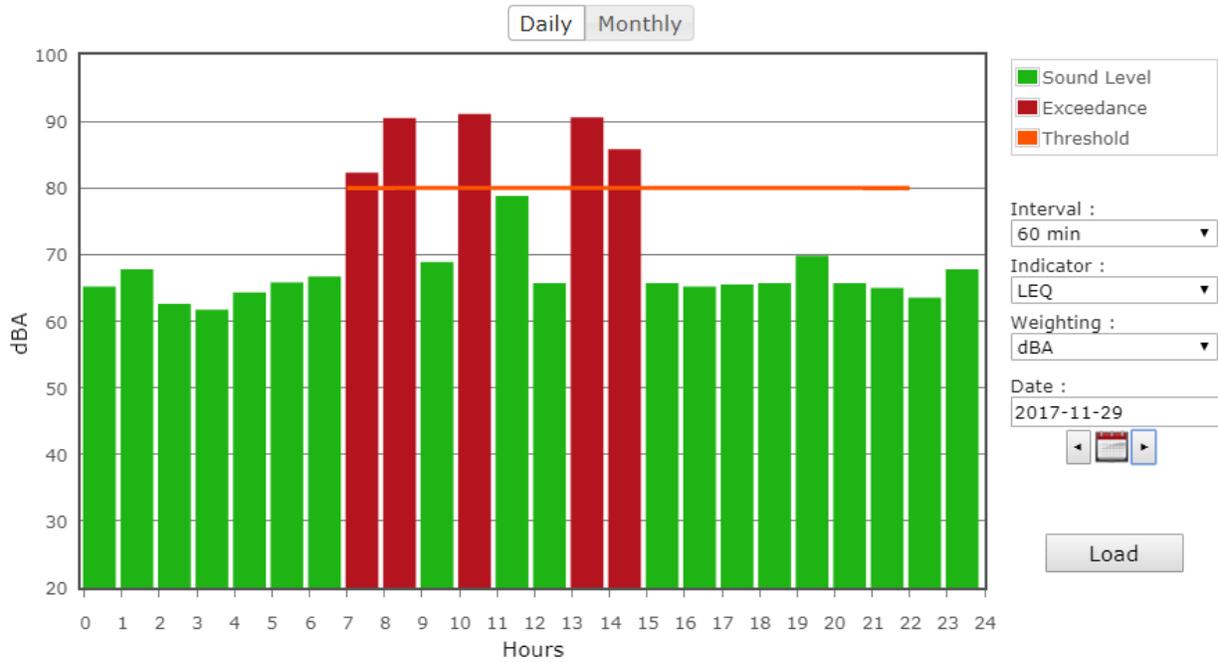


**Figure 14: Northeast Monitor NM-3 on Wednesday**

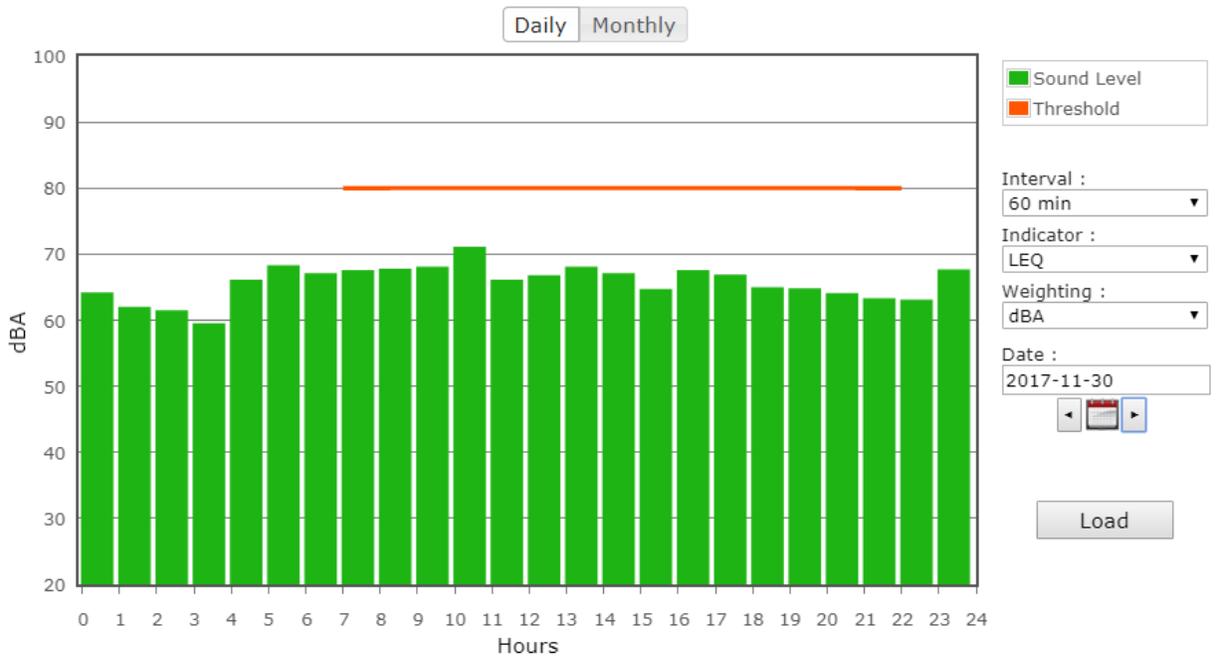


**Figure 15: Northeast Monitor NM-3 on Thursday**

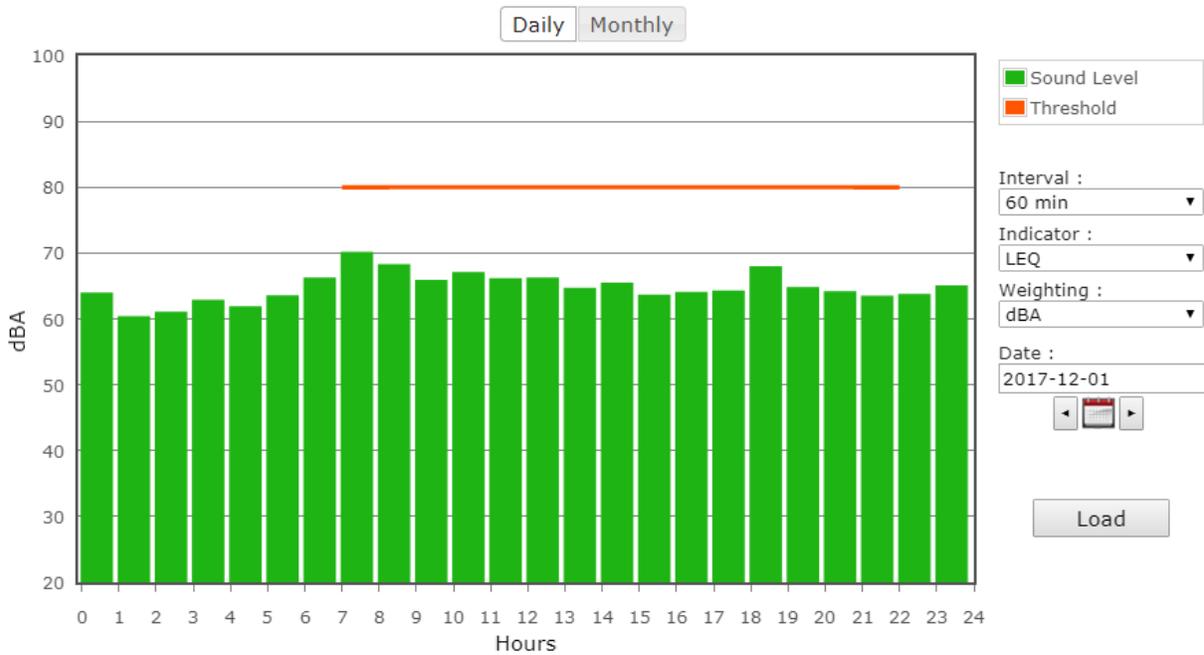


**Figure 16: Northeast Monitor NM-3 on Friday**

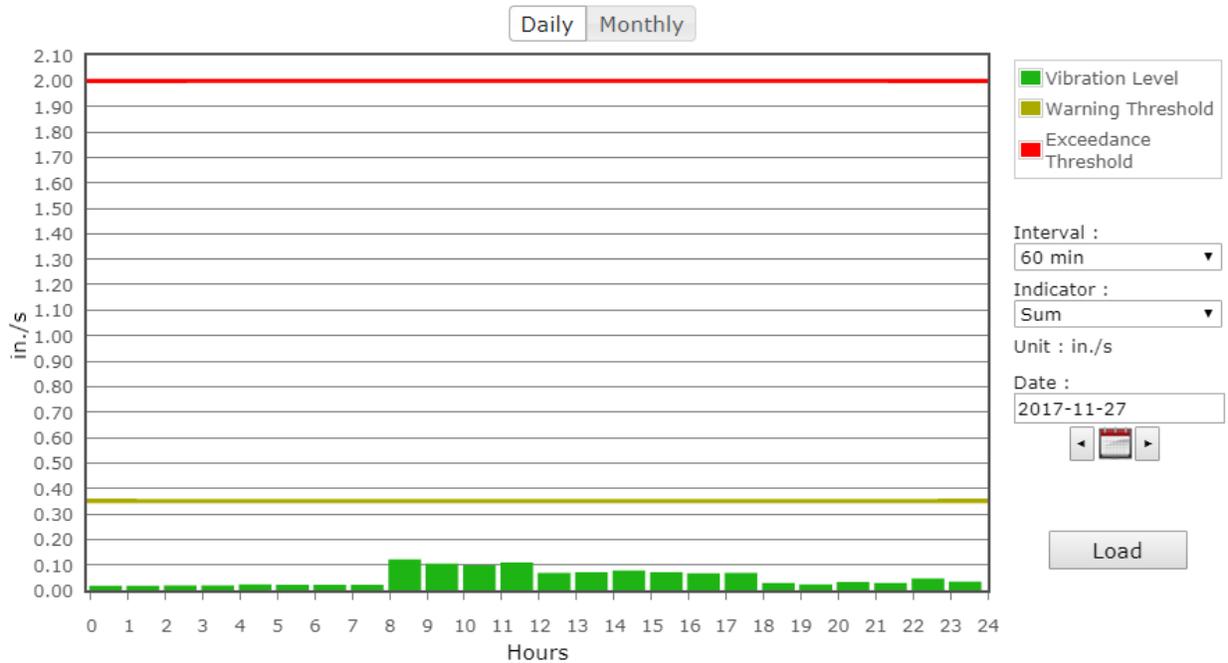


**Figure 17: North Vibration Monitor VM-1 on Monday**

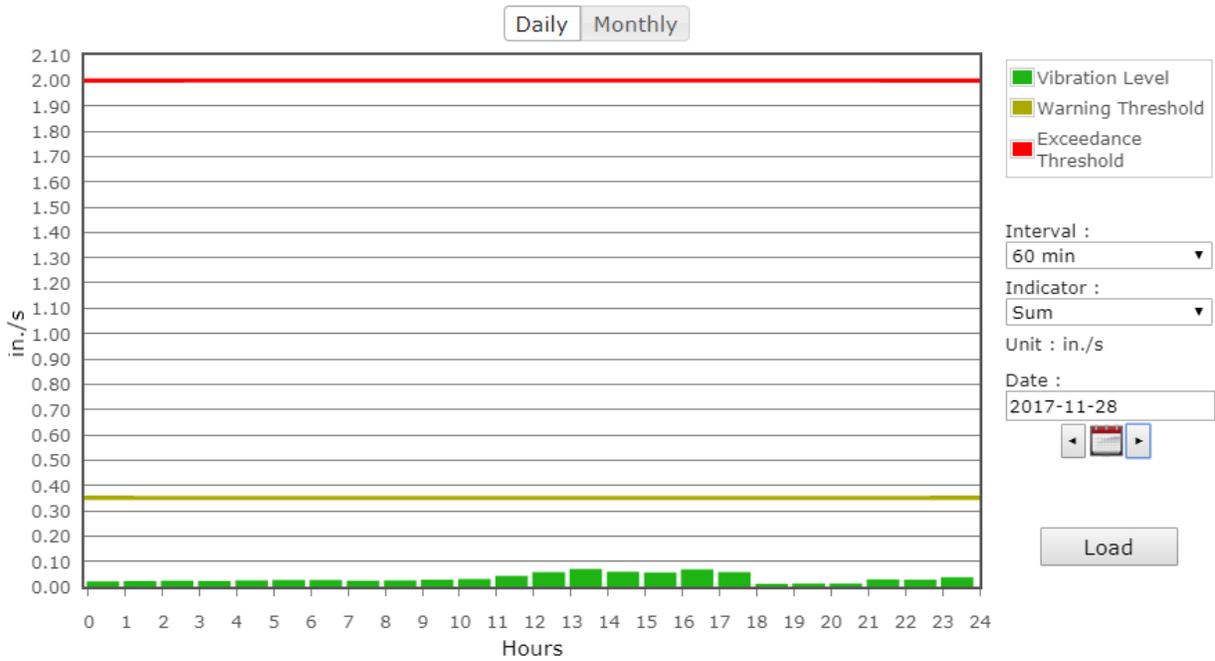


**Figure 18: North Vibration Monitor VM-1 on Tuesday**

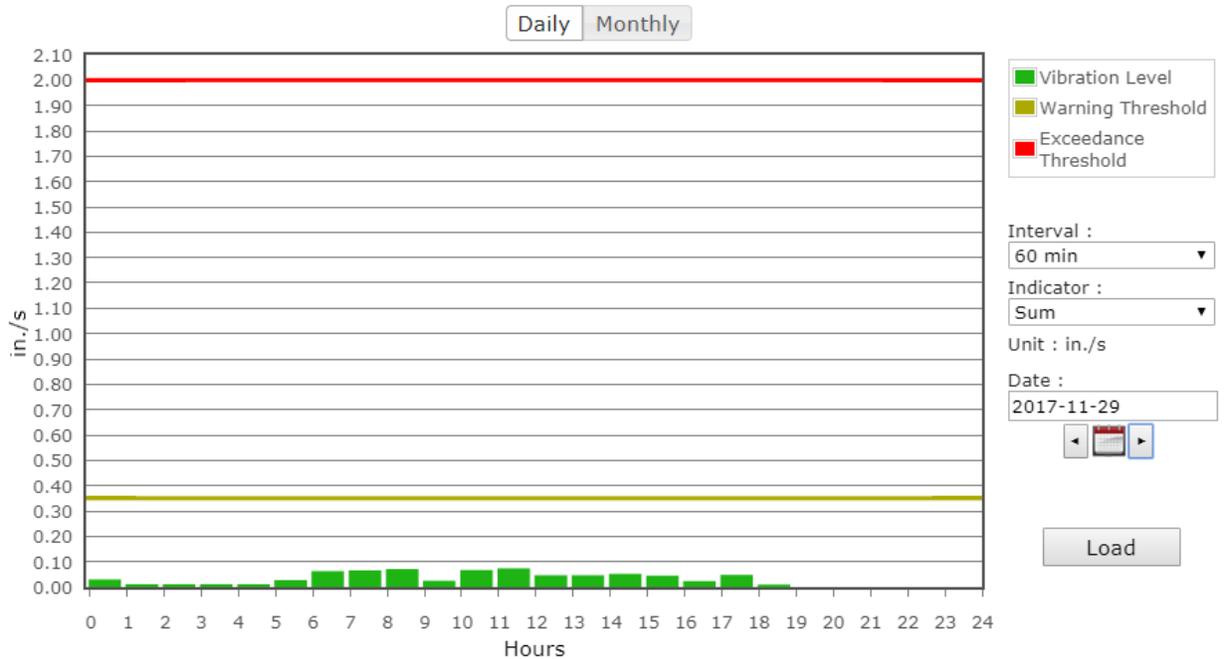


**Figure 19: North Vibration Monitor VM-1 on Wednesday**

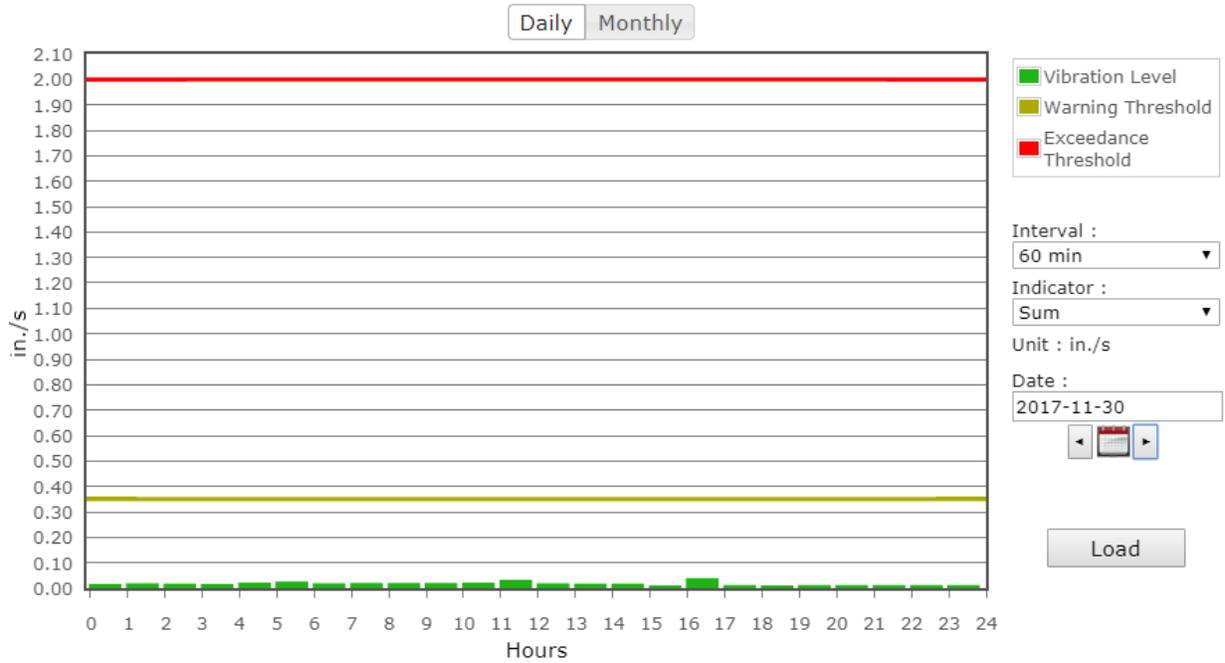


**Figure 20: North Vibration Monitor VM-1 on Thursday**

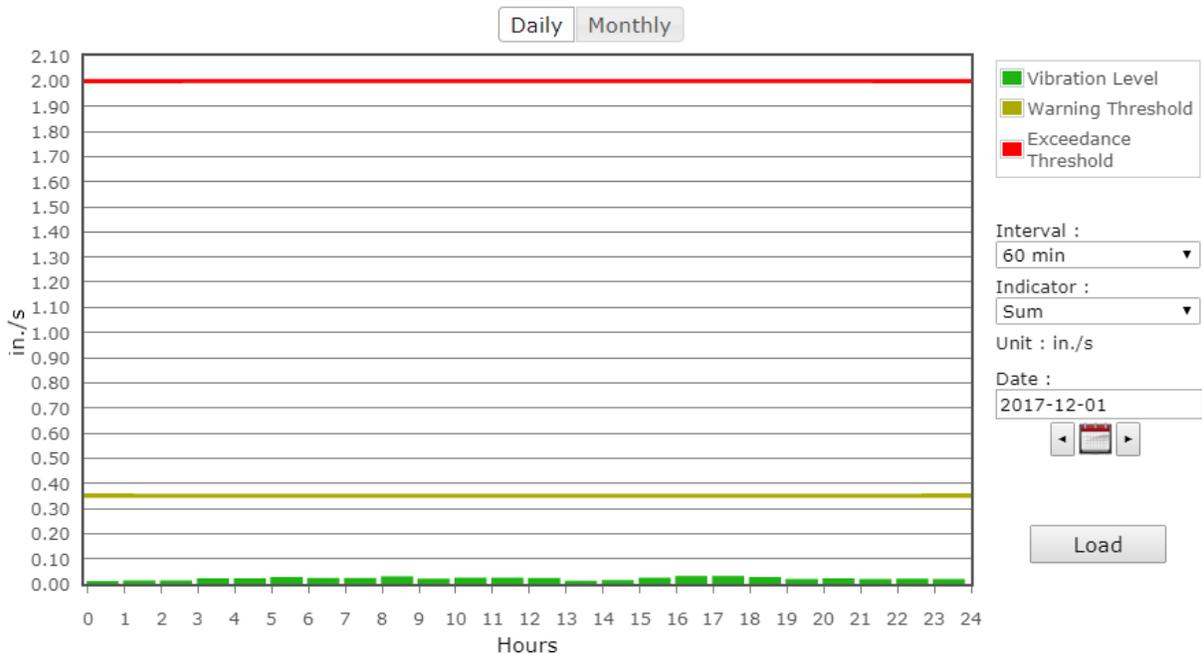


**Figure 21: North Vibration Monitor VM-1 on Friday**

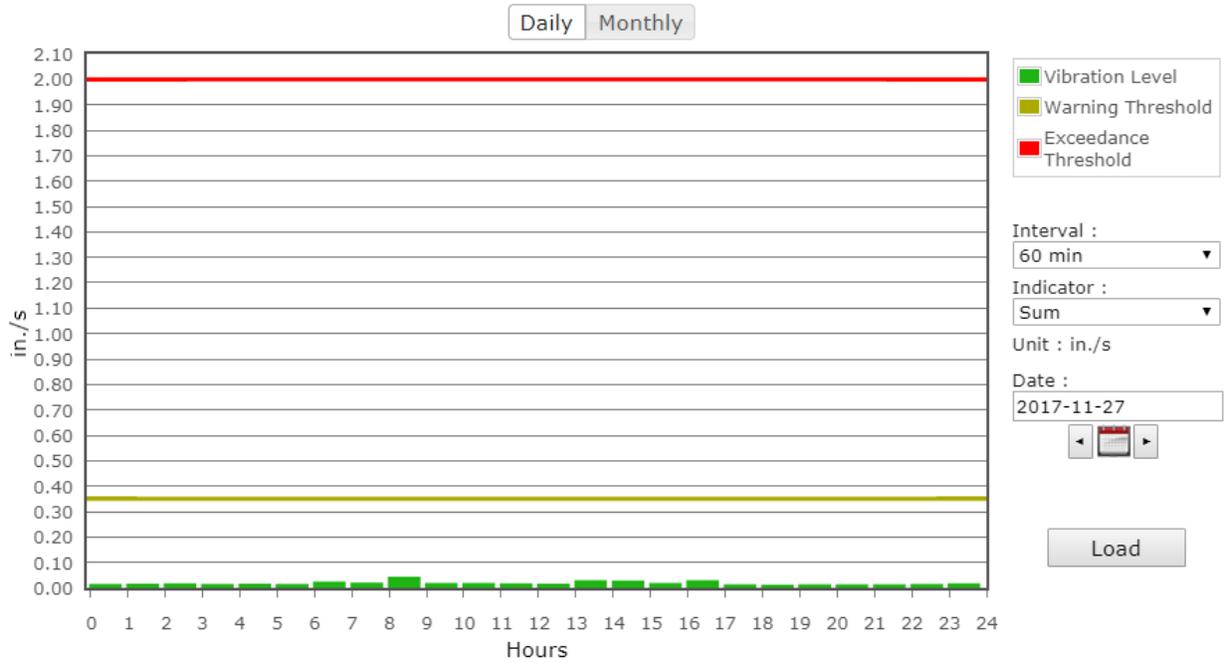


**Figure 22: South Vibration Monitor VM-2 on Monday**

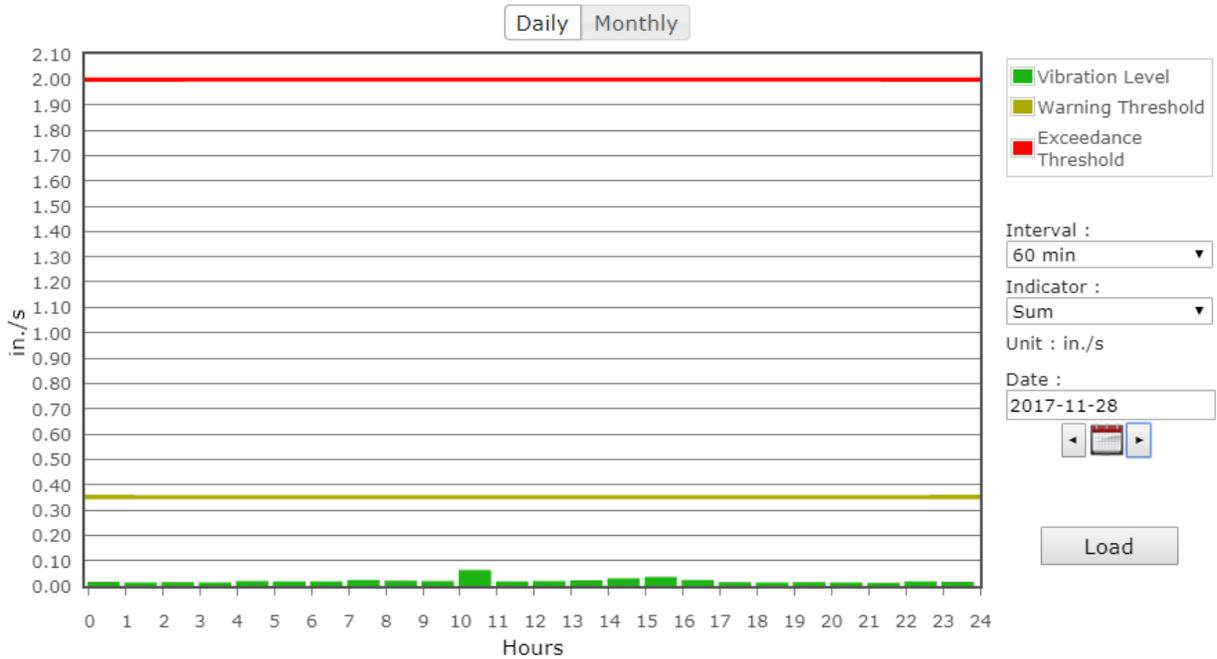


**Figure 23: South Vibration Monitor VM-2 on Tuesday**

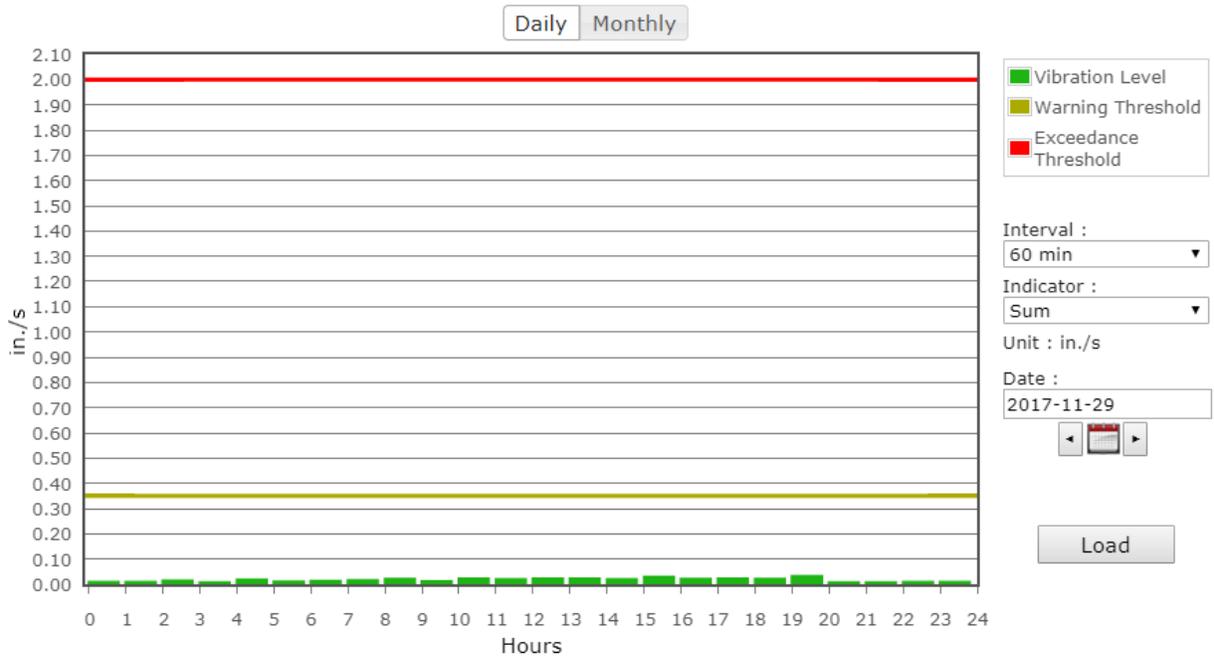

**Figure 24: South Vibration Monitor VM-2 on Wednesday**

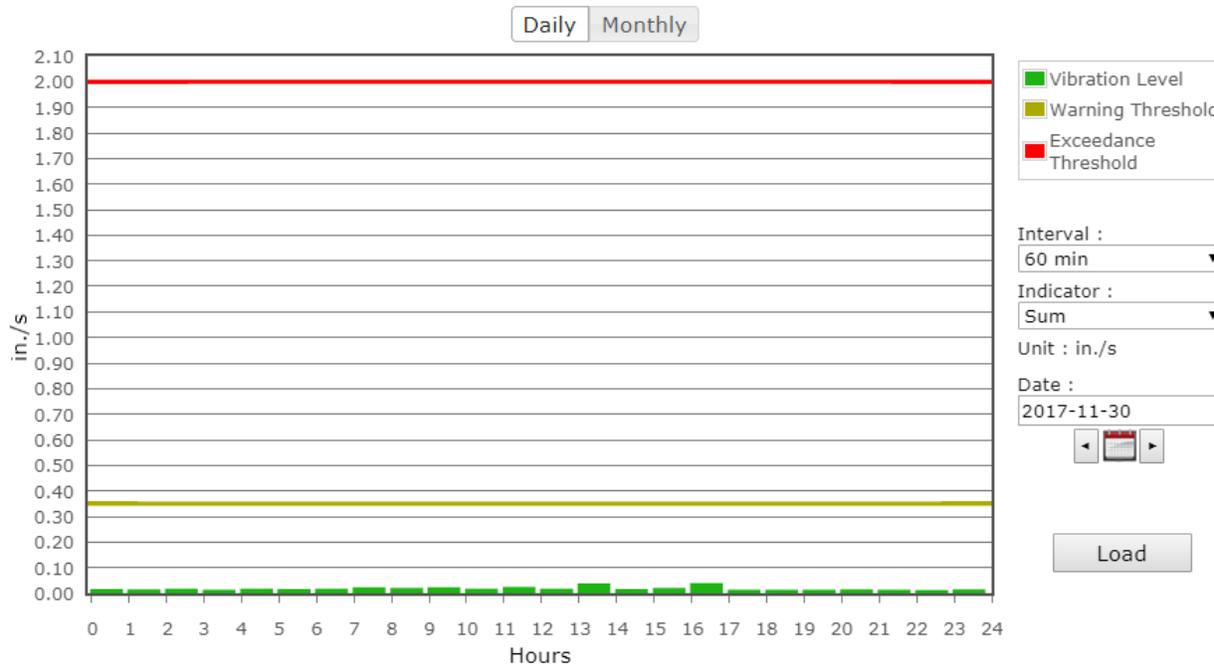

**Figure 25: South Vibration Monitor VM-2 on Thursday**

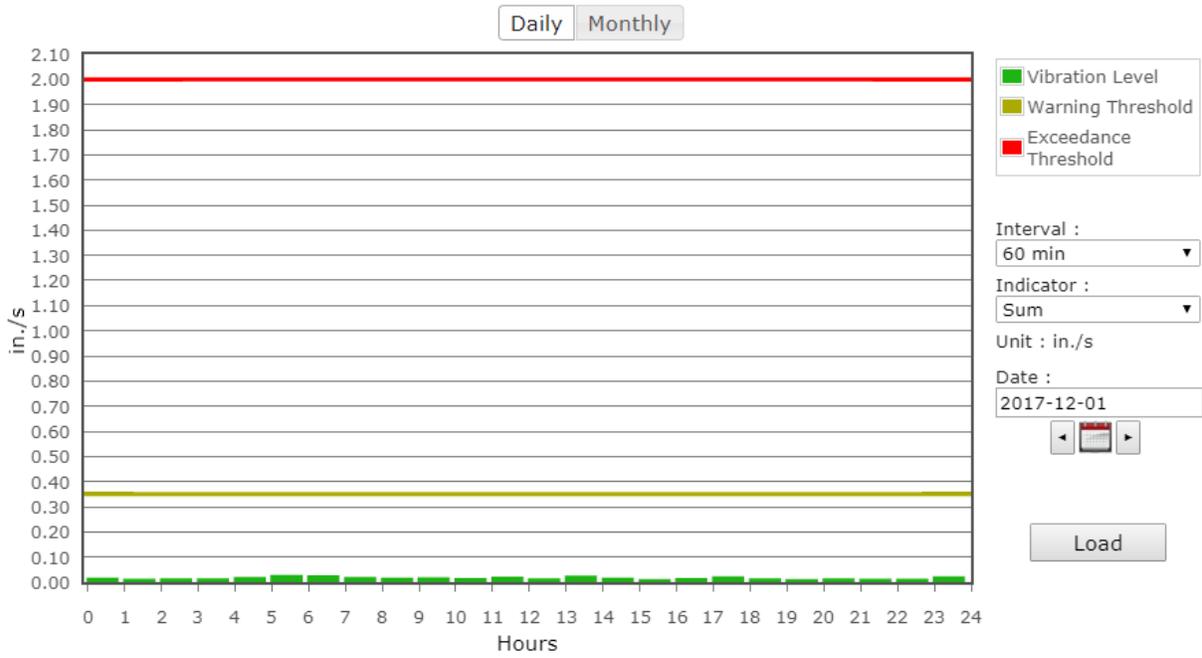

**Figure 26: South Vibration Monitor VM-2 on Friday**

20171204 Wilson Ihrig Weekly Noise and Vibration Report 27 Nov - 01 Dec 2017.docx

**AHRS WEEKLY REPORT**  
**(NO ACTIVITIES DURING CURENT WEEK)**



**WATER TREATMENT SYSTEM MONITORING LABORATORY ANALYTICAL DATA  
(NO ACTIVITIES DURING CURRENT WEEK)**



**CUMULATIVE DREDGED MATERIAL CHART  
(NO ACTIVITIES DURING CURENT WEEK)**

